



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 03.05.2021

### THIS WEEK

- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 3 & 4
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2, 3 & 4
- Ceiling grid install continues in Area 3 & 4
- New gymnasium CMU wall installation continuing
- Ceiling tile installation continues in Area 1 & 2
- Light fixture installation continues in Area 1, 2 & 4
- Handicap ramp installation continues in Area 4
- Fixed seating installation continues
- Fireproofing continues
- Roof deck installation continues at new gym
- Exterior masonry continues at new gym
- Storefront installation in Area 2

### NEXT WEEK: 03.08.21 – 03.12.21

- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 3 & 4
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2, 3 & 4
- Ceiling grid install continues in Area 3 & 4
- New gymnasium CMU wall installation continuing
- Ceiling tile installation continues in Area 1 & 2
- Light fixture installation continues in Area 1, 2 & 4
- Handicap ramp installation continues in Area 4
- Fixed seating installation continues
- Fireproofing continues
- Roof deck installation continues at new gym
- Exterior masonry continues at new gym
- Epoxy flooring in restrooms begins
- Flooring prep continuing

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status


\$4,860,760.45

Completed By:  
Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates

Storefront  
installation

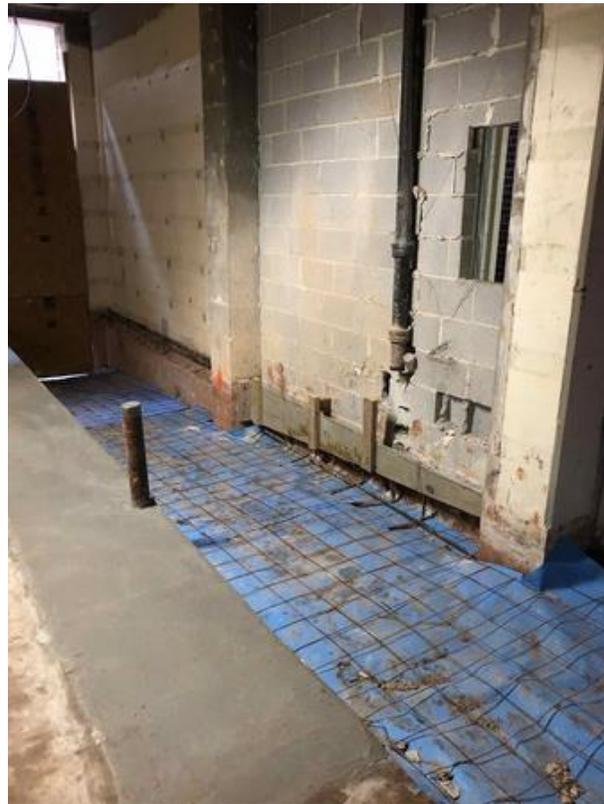

Handicap ramp  
installation

HVAC Unit Install



Cabinet Install 
