



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 04.09.2021

THIS WEEK

- HVAC relocation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 3 & 4
- Fire suppression continuing in Area 3 & 4
- New gymnasium CMU wall installation finishing
- Ceiling tile installation continues in Area 3 & 4
- Light fixture installation continues in Area 4
- Storefront installation at Media Center continues
- New gym brick continues
- Plumbing fixture installation continues
- Ceramic wall tile installation continues
- VCT installation continues
- Casework install continues
- Glazing installation continues
- New gym HVAC installation
- Toilet partitions and accessories install in Area 1 and 2
- EIFs at secure vestibule

NEXT WEEK: 04.12.21 – 04.16-21

- HVAC relocation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 3 & 4
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2, 3 & 4
- Ceiling tile installation continues in Area 3 & 4
- Light fixture installation finishing in Area 4
- Storefront installation at Media Center continues
- Plumbing fixture installation continues
- VCT installation continues
- Toilet Partitions and accessories installation continues
- Ceramic wall tile installation continues
- Casework install continues
- New gym brick continues
- New gym HVAC installation continues
- Glazing installation continues

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$7,256,108.62

Completed By:
Ben Fairchild


PARRISH
CONSTRUCTION GROUP

Photo Updates

New gym soffit framing



Vestibule ceiling framing

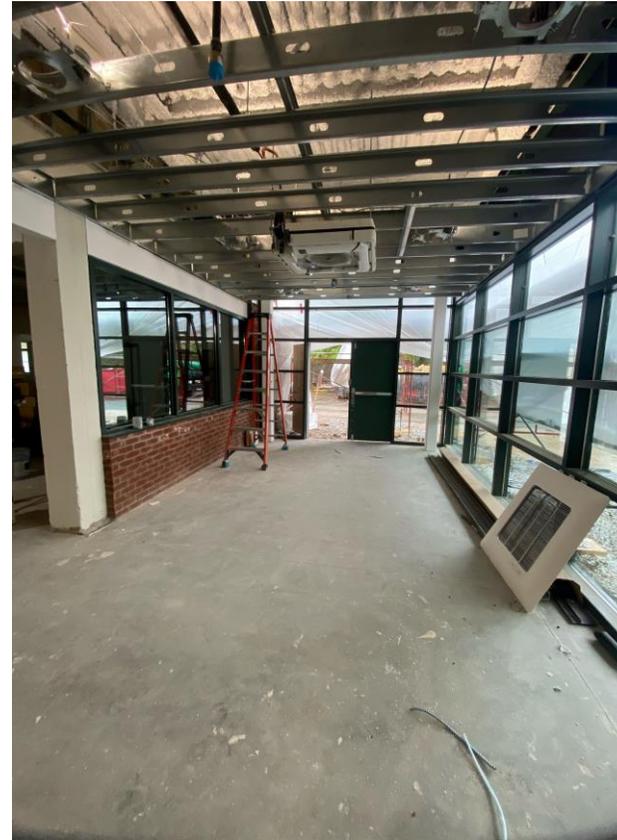

Toilet partition installation



EIFs at secure vestibule

