



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 04.30.2021

THIS WEEK

- Painting continuing in Areas 3 & 4
- Ceiling tile installation continues in Area 3 & 4
- VCT installation continues
- Ceramic wall tile installation continues
- Casework install continues
- New gym brick finishing
- Epoxy flooring continues
- Window installation at new gym continues
- New gym EIFs continues
- Interior painting at new gym continues
- Light fixture installation at new gym
- Clock installation
- Fixed seating at media center

NEXT WEEK: 05.03.21 – 05.07.21

- Painting continuing in Areas 3 & 4
- Ceiling tile installation continues in Area 3 & 4
- VCT installation continues
- Ceramic wall tile installation continues
- Casework install continues
- Epoxy flooring continues
- Window installation at new gym continues
- New gym EIFs continues
- Interior painting at new gym continues
- Light fixture installation at new gym continues
- Pressure washing new brick
- Fire riser installation beginning

BUDGET

Construction Budget

\$10,900,000.00

Budget Status


\$8,377,029.68

Completed By:
Ben Fairchild

PARRISH
CONSTRUCTION GROUP

Photo Updates

New gym light fixtures

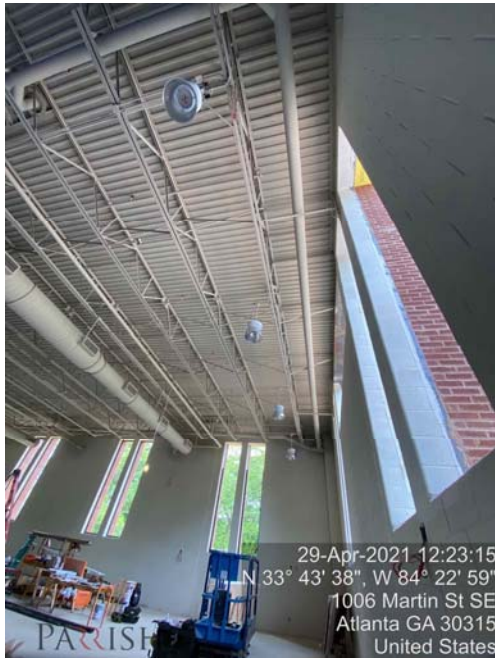

Media center fixed seating



New gym window frames



New gym interior painting

