



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 05.21.21

### THIS WEEK

- Touch-up painting continuing in Areas 3 & 4
- VCT installation continues
- Casework install continues
- Epoxy flooring continues
- Pressure washing new brick
- Floor base installation continues
- Carpet installation finishes
- Glazing installation finishes
- Exterior door installation continues at new gym
- New gym EIFs continues
- Polycarbonate panel installation at new gym
- HVAC control system installation
- Drinking fountain installation
- Kiln installation
- Electrical device trim out
- Storefront door installation begins
- Restroom plumbing fixture installation

### NEXT WEEK: 05.24.21 – 05.28.21

- Touch-up painting continuing in Areas 3 & 4
- VCT installation continues
- Casework install continues
- Floor base installation continues
- Electrical device trim out continues
- Storefront door installation continues
- Restroom plumbing fixture installation continues
- HVAC control system installation continues
- LVT installation begins
- New gym EIFs finishing

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$8,377,029.68

Completed By:  
Ben Fairchild

**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates


Storefront door installation



Polycarbonate window panel installation



Drinking fountain installation

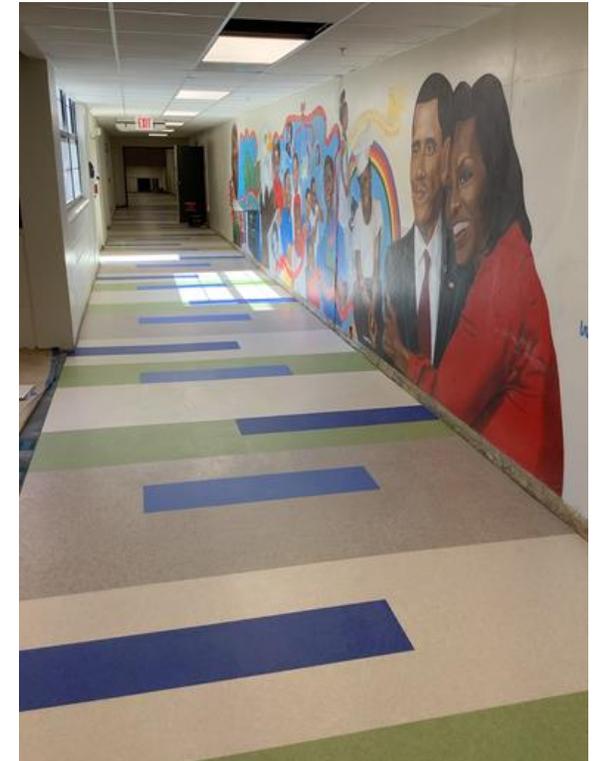

VCT installation

