



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 05.28.2021

### THIS WEEK

- Touch-up painting continuing in Areas 3 & 4
- VCT installation continues
- Floor base installation continues
- Electrical device trim out continues
- Storefront door installation continues
- Restroom plumbing fixture installation continues
- HVAC control system installation continues
- Exterior door installation continues
- Media center carpet installation finishes
- Access control installation begins
- LVT installation in reception area
- Walk off mat installation in front secure vestibule
- Interior signage completed

### NEXT WEEK: 05.31.21 – 06.04.21

- Floor base installation continues
- Electrical device trim out continues
- Restroom plumbing fixture installation finishing
- HVAC control system installation continues
- Door installation beginning
- Access control installation continues
- Final grading around new gymnasium
- New sidewalk installation begins
- Toilet partitions and accessories installation finishes
- Stair nosing and tread installation beginning

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$8,999,802.00

Completed By:  
Ben Fairchild

**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates


Walk off mat  
installation



Signage installation



Media center carpet  
installation

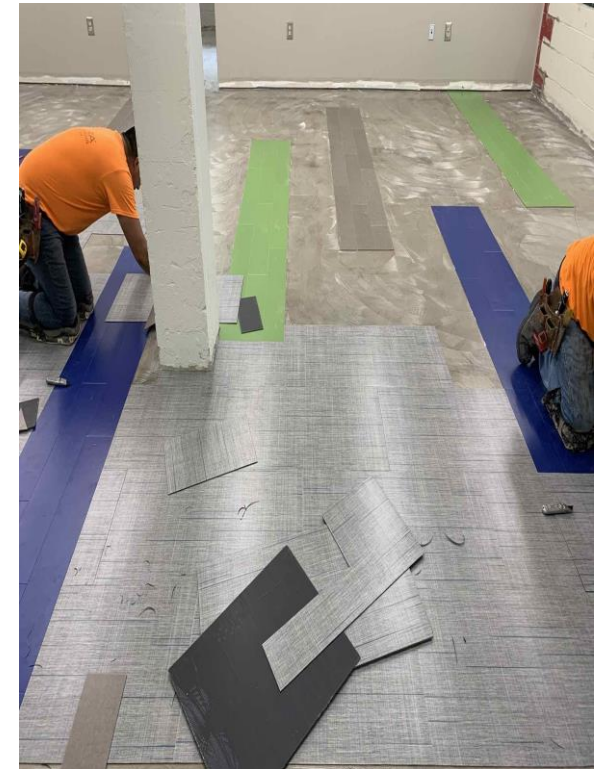

LVT installation

