



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 06.04.2021

### THIS WEEK

- Floor base installation continues
- Electrical device trim out continues
- Restroom plumbing fixture installation finishing
- Access control installation continues
- Final grading around new gymnasium
- New sidewalk installation continues
- Toilet partitions and accessories installation finishes
- Concrete stair installation at new gym
- LVT installation finishes
- Concrete demolition for parking lot

### NEXT WEEK: 06.07.21 – 06.11.21

- Floor base installation continues
- Electrical device trim out continues
- Restroom plumbing fixture installation finishing
- Access control installation continues
- Final grading around new gymnasium
- New sidewalk installation finishes
- Toilet partitions and accessories installation finishes
- Stair nosing and tread installation begins
- Gym floor installation begins
- Basketball goal and wall pad installation
- Final cleaning begins

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status


\$8,999,802.00

Completed By:  
Ben Fairchild


**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates


Sidewalk installation

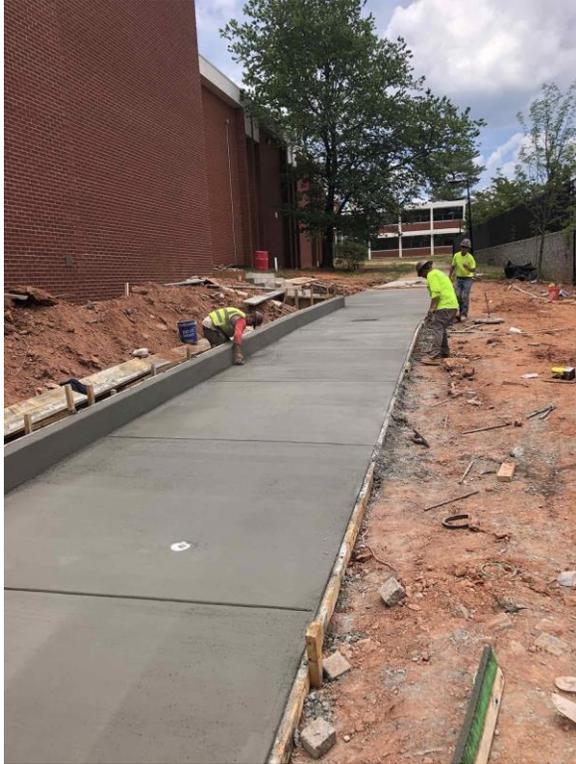

Concrete demolition for parking lot

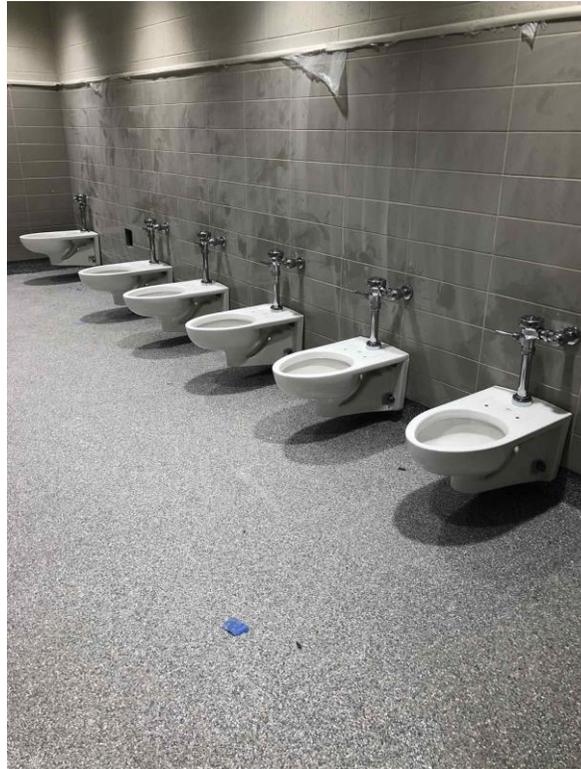

New gym Plumbing fixture installation

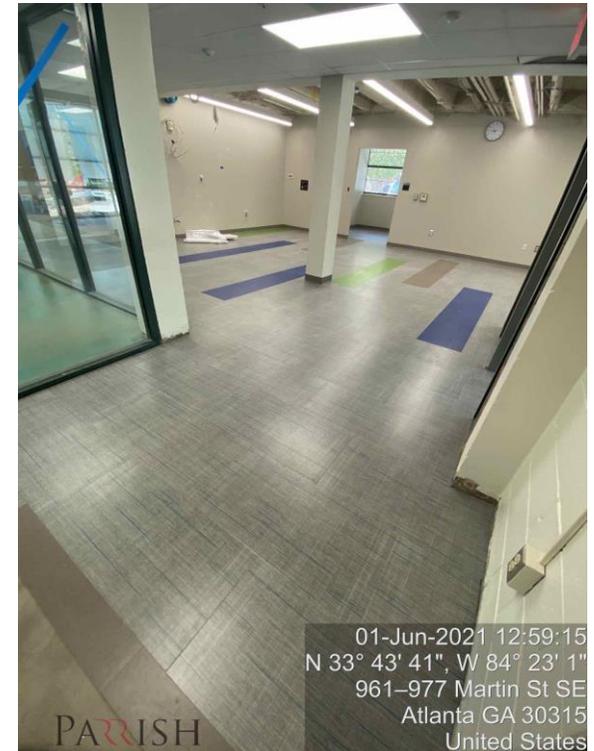

LVT installation complete

