



# **Weekly Construction Progress Report**

**Addition and Renovation work to  
Morningside Elementary School  
Week Ending: 06/04/2021**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## Upcoming Activities

- Week of June 7<sup>th</sup>
  - Interior demolition continues
    - Includes dumpsters
  - Demolition of existing gym continues
  - Sitework begins
    - Includes large equipment deliveries and dump truck traffic
    - Tree removal
    - Storm structure delivery
- Week of June 14
  - Demolition of existing gym finishes
  - Interior demolition continues
  - Sitework continues
    - Tree removal continues
    - Storm structure installation begins
- Week of June 21
  - Sitework continues
  - Interior demolition continues
  - Building pad grading
    - Includes bulldozers, dump trucks and other heavy equipment



# Budget

## BUDGET

### Construction Budget

- \$17,100,000

### Budget Status

- \$540,639.28



## ADDITIONAL INFO

- Completed By
  - Ben Fairchild
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Jim Fallon, PCG
  - A.J. Segel, PCG
  - Chris Hubbard, PCG





# Photo/Activity Updates

Interior demolition




Concrete demolition at existing gym building





# Photo Updates

Interior demolition

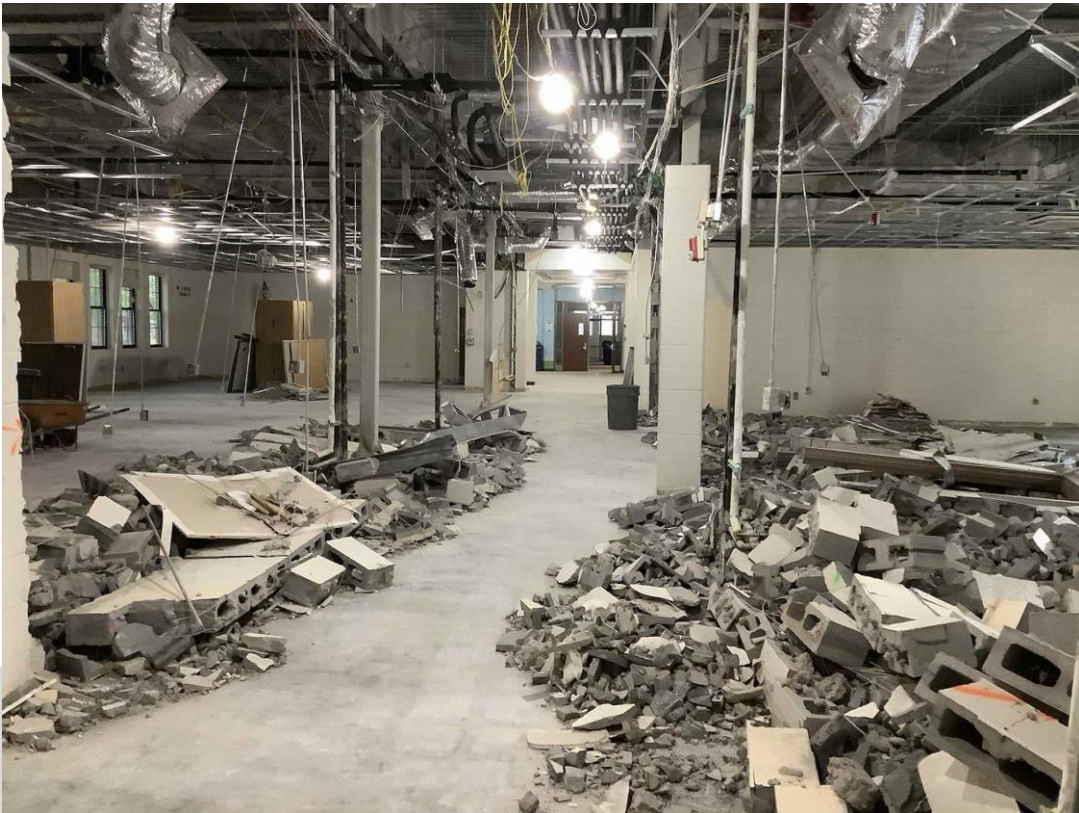

Existing gym concrete slab demolition





# Photo Updates

Interior demolition



Existing gym building demolition

