



# **Weekly Construction Progress Report**

**Addition and Renovation work to  
Morningside Elementary School  
Week Ending: 06/11/2021**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## Upcoming Activities

- Week of June 14<sup>th</sup>
  - Demolition of existing gym retaining wall
  - Interior demolition continues
    - Electrical demolition
    - Existing HVAC demolition
  - Sitework continues
    - Tree removal continues
    - Storm structure installation begins
    - Includes excavators, dump trucks and other heavy equipment
- Week of June 21
  - Sitework continues
    - Site storm drainage begins
  - Interior demolition continues
  - Building pad grading
    - Includes bulldozers, dump trucks and other heavy equipment
- Week of June 28
  - Sitework continues
  - Interior demolition finishes
  - Building pad grading continues



# Budget

## BUDGET

### Construction Budget

- \$17,100,000

### Budget Status

- \$540,639.28



## ADDITIONAL INFO

- Completed By
  - Ben Fairchild
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Jim Fallon, PCG
  - A.J. Segel, PCG
  - Chris Hubbard, PCG





# Photo/Activity Updates

Existing gym building demolition complete




Existing gym building demolition complete





# Photo Updates

Interior demolition at existing cafeteria

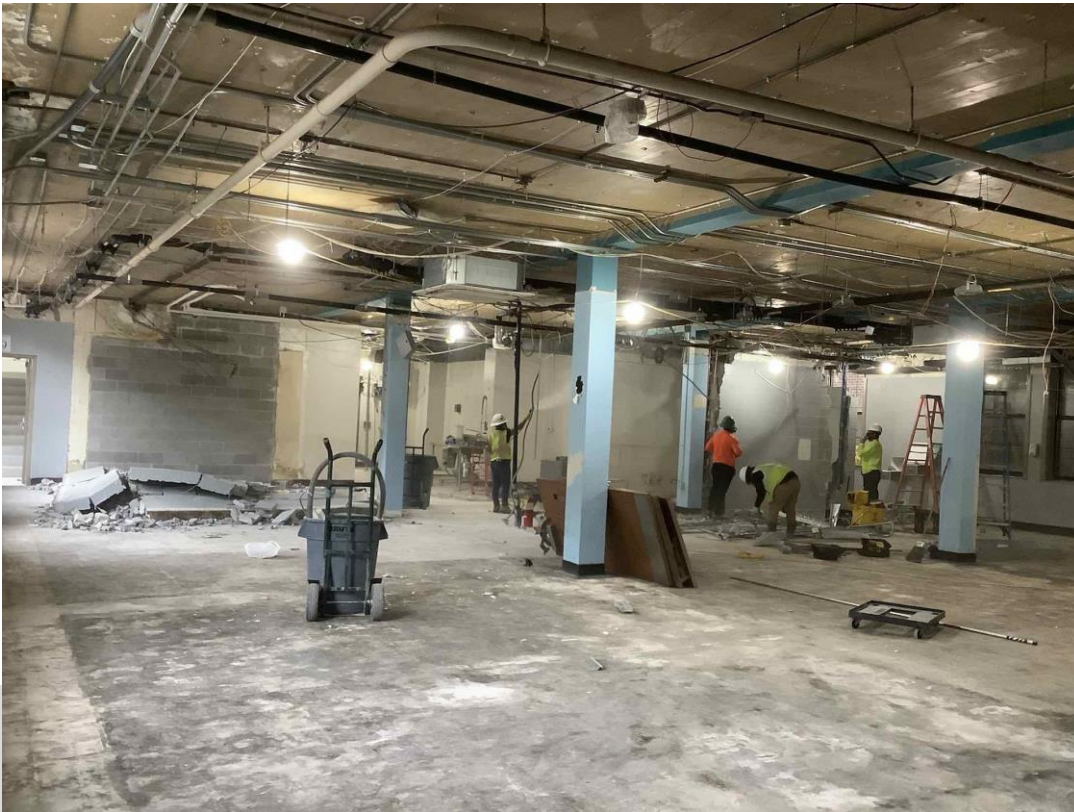

Interior demolition at media center





# Photo Updates

Existing turf removal



Storm structure delivery

