



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 06.18.2021

THIS WEEK

- Floor base installation continues
- Stair nosing and tread installation begins
- Gym floor installation
- Final cleaning continues
- Stair handrail installation continues
- Fencing begins
- Modular wall at gymnasium parking lot begins
- Curb and gutter installation at new gym
- Toilet partitions and accessories installation finishes
- Landscaping begins
- Gymnasium wall pad installation
- Basketball goal installation
- Floor waxing in Area 1

NEXT WEEK: 06.21.21 – 06.25.21

- Floor base installation continues
- Stair nosing and tread installation continues
- Final cleaning continues
- Stair handrail installation finishes
- Parking lot grading continues at gymnasium
- Fencing continues
- Modular wall at gymnasium parking lot finishes
- Landscaping continues
- Incline lift installation begins
- Gymnasium wall pad installation
- Door installation
- Sidewalk installation at new gym

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$8,999,802.00

Completed By:
Ben Fairchild

PARRISH
CONSTRUCTION GROUP

Photo Updates


Curb and gutter installation at gym



Landscaping



Gym floor installation

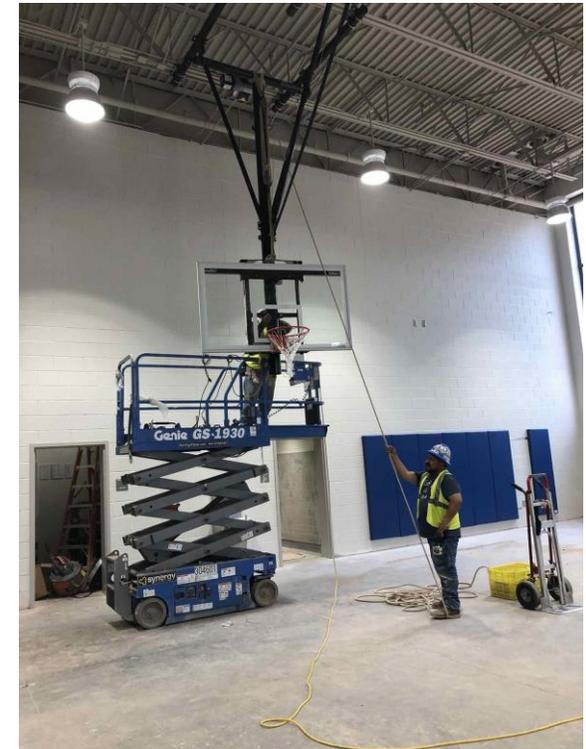

Basketball goal installation

