



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 07/02/2021

THIS WEEK

- Final cleaning continues
- Fencing continues
- Landscaping continues
- Incline lift installation
- Doors and hardware installation
- Asphalt paving at new gym complete
- Pavement striping and marking finishes
- Floor waxing continues
- Concrete apron installation at new gym
- Handrail installation continues
- Plaque installation
- Fire extinguisher and cabinet installation
- Wall pack replacement
- Toilet partitions and accessories installation
- Building final inspection begins

NEXT WEEK: 07.05.21 – 07.09.21

- Final cleaning continues
- Fencing continues
- Landscaping continues
- Doors and hardware installation
- Floor waxing continues
- Handrail installation continues
- Toilet partitions and accessories installation finishes

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$9,927,049.15

Completed By:
Ben Fairchild


PARRISH
CONSTRUCTION GROUP

Photo Updates

Concrete stairs at new gym



Incline lift installation

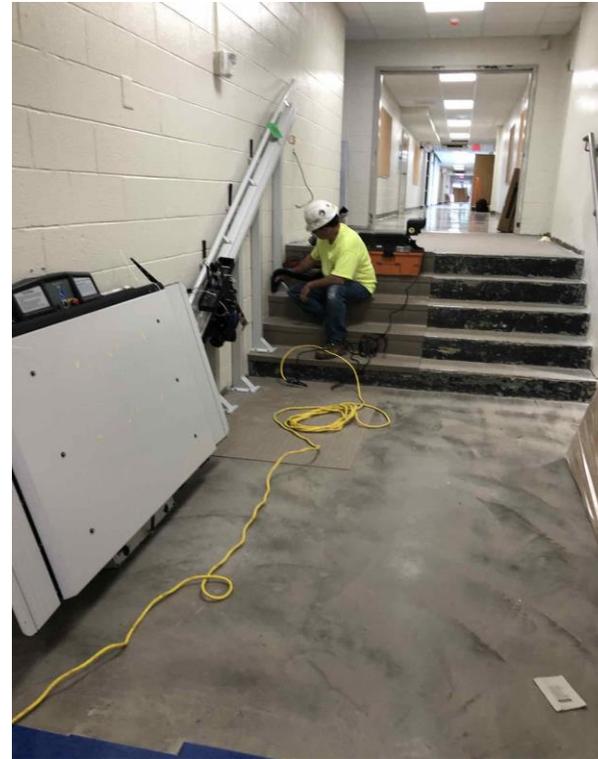

Dimensional letter signage



Asphalt paving

