



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 07/23/2021

THIS WEEK

- Sitework
 - Storm drainage piping installation
- Mechanical demolition continues throughout building
- Electrical demolition continues throughout building
- Electrical overhead rough-in begins in area A and B
- Plumbing rough-in continues throughout building
- Interior demolition continues in area B
- Plumbing underground rough-in continues at area B

NEXT WEEK: 07.26.21 – 07.30.21

- Sitework
 - Storm drainage piping installation
 - Building pad grading begins
- Interior wall framing begins in area A
- Mechanical demolition continues throughout building
- Electrical demolition continues throughout building
- Interior demolition finishes
- Mechanical rough-in begins in area B
- Electrical rough-in continues in area A and B
- Plumbing rough-in continues throughout building
- Plumbing underground rough-in at area B complete

BUDGET

Construction Budget

\$17,600,000.00

Budget Status

\$894,522.11

Completed By:
Ben Fairchild

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

Mechanical demolition



Selective slab demolition



Photo/Activity Updates

Underground plumbing rough-in




Underground plumbing rough-in



Photo/Activity Updates

Electrical overhead rough-in

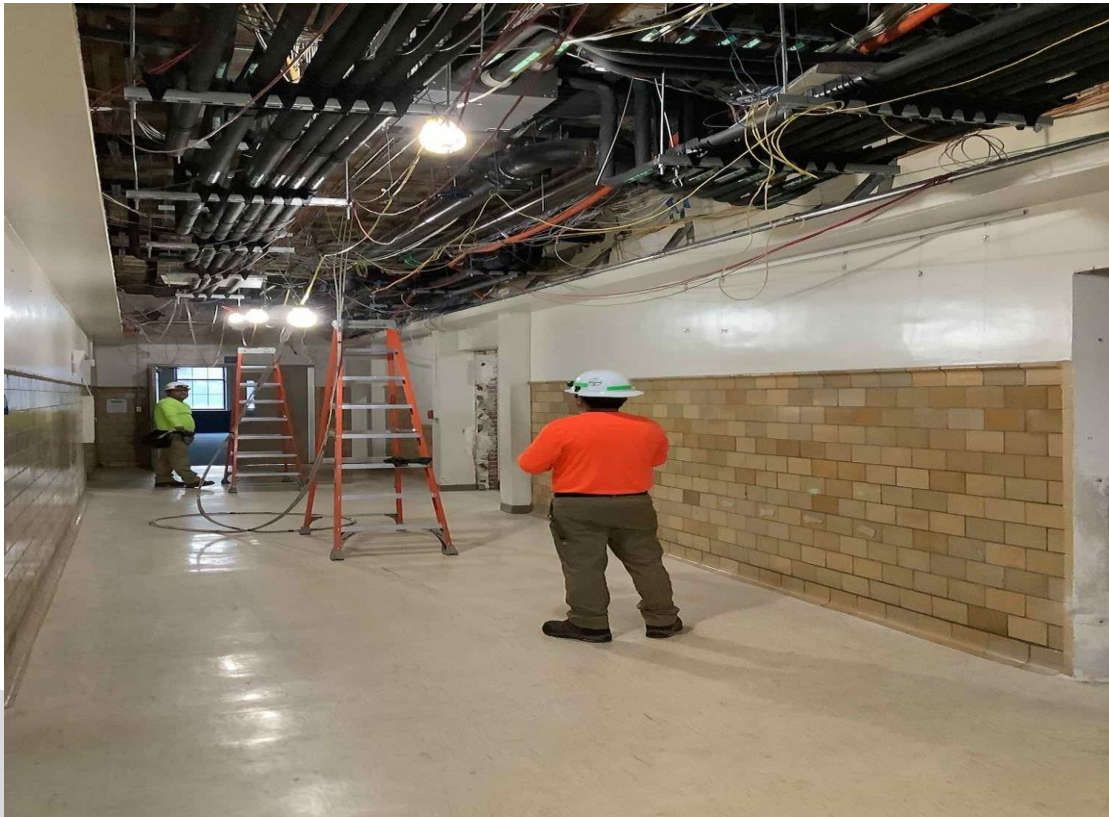

Electrical overhead rough-in



Photo/Activity Updates

Sitework



Site storm drainage line installation

