



# Weekly Construction Progress Report

## Morningside Elementary School

Week Ending: 10/29/2021

### THIS WEEK

- Sitework continues
  - Site grading
- Mechanical equipment relocation continues
- Mechanical, electrical and plumbing rough-in continues throughout building
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Door frame installation continues
- Batt insulation installation continues
- Concrete for new gym footings
- New gym underground utilities continues
- Lighting installation begins in Area A
- Ceiling grid installation begins
- Carpet demolition at auditorium
- Hollow metal window frame installation

### NEXT WEEK: 11.01.21 – 11.05.21

- Sitework continues
  - Site grading
- Mechanical equipment relocation continues
- Mechanical, electrical and plumbing rough-in continues throughout building
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Door frame installation continues
- Batt insulation installation continues
- New gym underground utilities continues
- Lighting installation continues
- Ceiling grid installation continues
- Hard ceiling rough-in begins
- Interior painting begins at Area A

### BUDGET/SCHEDULE

#### Construction Budget

\$17,600,000.00

#### Budget Status

\$2,395,124.47

#### Substantial Completion:

July 25, 2022

#### Schedule Status:

On Schedule

Completed By:

Ben Fairchild

**PARRISH**  
CONSTRUCTION GROUP

# Photo/Activity Updates

Hollow metal window frame installation




Ceiling grid installation



# Photo/Activity Updates

Plumbing underground rough-in at new gym

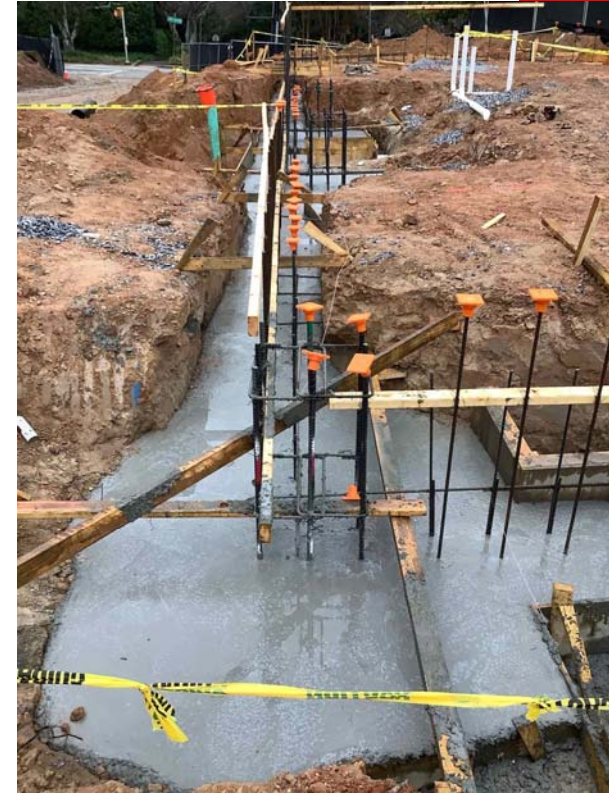

Concrete pour for remaining new gym footings





# Photo/Activity Updates

VRF installation



Interior lighting installation

