



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 11/19/2021

THIS WEEK

- Fire line installation completed
- Mechanical equipment relocation continues
- Mechanical and electrical rough-in continues throughout building
- Low voltage rough-in continues
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues
- Ceiling grid installation continues
- Hard ceiling installation begins
- Interior painting begins at Area A
- Exterior metal stud installation at cafeteria addition
- Waterproofing at cafeteria
- Cafeteria addition decking install
- Retaining wall footing install at cafeteria
- New gas service install

NEXT WEEK: 11.22.21 – 11.26.21

- Mechanical equipment relocation finishing
- Mechanical and electrical continues throughout building
- Low voltage rough-in continues
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A
- Exterior cafeteria studs and sheathing continues.
- Cafeteria addition decking finishing
- Cafeteria addition retaining wall footings continues
- Thanksgiving Break 11/25-11/26

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$5,851,249.24

Substantial Completion:

July 25, 2022

Schedule Status:

On Schedule

Completed By:

Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

Cafeteria retaining wall install



New gas line to COPS Building



Photo/Activity Updates

Cafeteria addition decking install




Waterproofing at cafeteria addition



Photo/Activity Updates

Acoustical insulation install

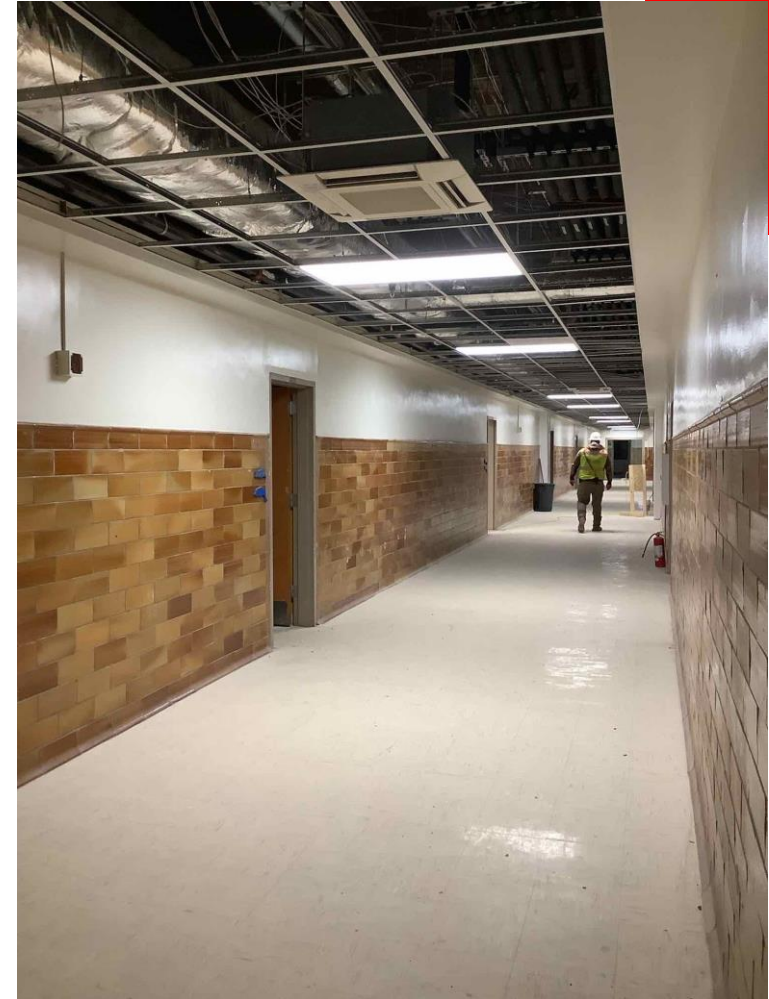

New lighting install



Photo/Activity Updates

Electrical rough-in



Mock-up room

