



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 01/07/2022

THIS WEEK

- Mechanical and electrical rough-in continues throughout building
- Low voltage rough-in continuing
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A and Area B
- Steel erection continuing at new addition
- Replacement of standing seam metal roof continuing
- Second floor decking installation continues

NEXT WEEK: 01.10.22 – 01.14.22

- Mechanical and electrical continues throughout building
- Low voltage rough-in continues
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A and Area B
- Steel erection continuing at new addition
- Second floor decking installation finishes
- Second floor concrete slab placement
- Replacement of standing seam metal roof continuing

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$7,885,894.73

Substantial Completion:

July 25, 2022

Schedule Status:

On Schedule

Completed By:

Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

New addition structural steel




Structural steel install



Photo/Activity Updates

New addition structural steel

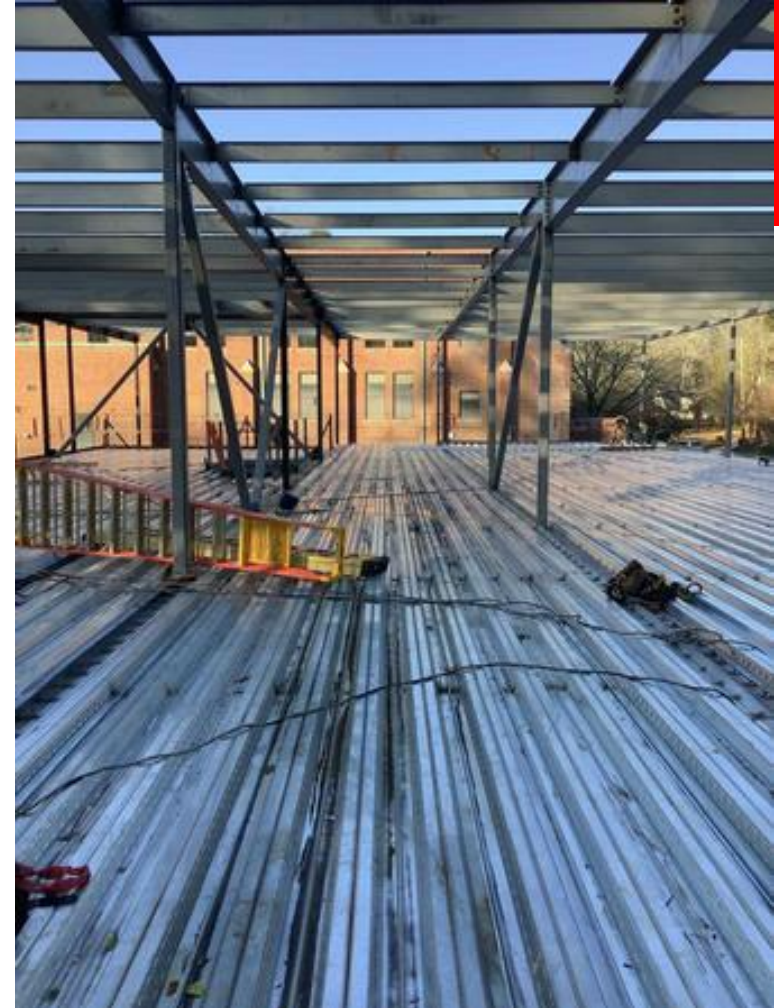

Second floor decking install



Photo/Activity Updates

Cafeteria courtyard stair installation



CMU installation at addition



Photo/Activity Updates

Roof drain piping at cafeteria addition



Restroom hard ceiling install



Photo/Activity Updates

Sprinkler pipe installation



Kitchen ductwork installation

