


WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Woodson Park Academy & YMCA-ELC
Week Ending: May 15th, 2020

THIS WEEK:

- Masonry and Brick continues at WPA
 - MEP Overhead continues at WPA
 - Framing continues at WPA
 - Steel at YMCA continued
 - Site Sub working on LL site utilities
 - Fireproofing at media center
 - COA inspections – delays occurring due to COVID-19 action
-

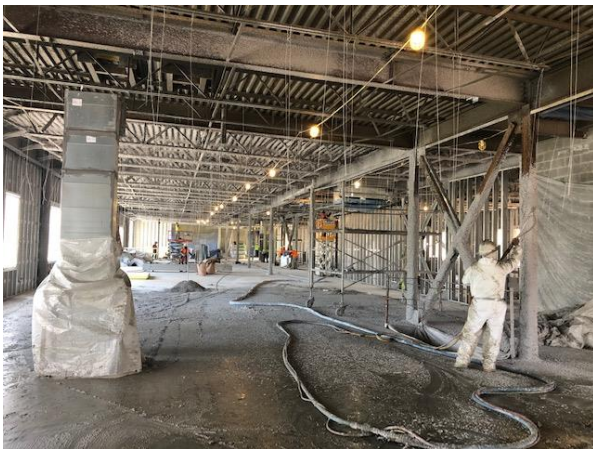

Fireproofing 3rd floor WPA



Roof decking at the YMCA



Brick on the NE side of WPA



Bus loop ready for curb and gutter



WEEKLY CONSTRUCTION PROGRESS REPORT



Exterior framing at YMCA started



Interior framing at WPA

NEXT WEEK – May 18th thru May 22nd:

- Masonry and Brick continues
- MEP Overhead continues
- Framing continues
- Storefront Frames and Glass install to begin at WPA
- LL Utilities continue
- Structural Steel at YMCA continues
- Exterior Framing at the YMCA
- Fireproofing at Media Center
- COA inspections – delays occurring due to COVID-19 action

PAYMENT STATUS:

- Gmp#1 \$3,703,488.00
 - Paid to date amount \$2,129,067.57
- GMP#2 \$27,034,273.00
 - Paid to date amount \$8,523,875.14
- GMP#3 \$5,877,688.00
 - Paid to date amount \$0.00
- GMP#4 \$1,974,712.00
 - Paid to date amount \$0.00

WEATHER:

- Total of 0" of rain for the week

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- WPA – November 4, 2020
- YMCA-ELC - November 12, 2020

PREPARED BY:

- **Matt Dauber, Carroll Daniel Construction Co.**

