

BENTEEN

ELEMENTARY SCHOOL

*Weekly Construction Progress Report
Week 05/1/2023-05/5/2023*



Balfour Beatty

Current Activities 05/1/23-05/5/23

- Installation of electrical shut off switches for VRF system at area D and E.
- Prepping Floor for Epoxy in Area E – Complete
- Kitchen Epoxy - Complete
- Installation of low voltage data drops in Area A,B,C
- Install Bathroom Fixtures – Complete
- Install Lights & low volt in ceiling grid in area A, B, C
- Insulation of Ductwork In Area E - Complete
- Install Corridor Lights – Ongoing
- Cut Ceiling Tile Border
- Install Toilet Partitions – Complete
- Final Coat of Finish Paint and Accent walls in Area B,C
- Paint Bathroom Ceilings
- Install Brick Screen wall at HVAC pad – Complete
- Install Gas line on roof – Complete
- Offsite Planting – Complete
- Install Ceiling Tile in Area A – Complete
- Room 1110 Drywall Install - Complete
- Vestibule Framing – Complete
- Monument Sign Footing and Brick/Cast stone - Complete

Upcoming Activities 05/8/23-05/12/23

- Final Coat of Finish Paint remaining Areas
- Install Ceiling Grid in Area E, Kitchen, and Cafeteria
- Install Ceiling Tile Area C
- VCT Flooring Install Area E
- LED Monument Sign install
- Pressure washing Exterior of building



Monument Sign Cast Stone and Brick
Installed



Vestibule and Canopy sidewalk concrete
poured

Progress Photos




Ceiling Grid Install in Area A




HVAC Units Masonry Screen wall
Installed



Onsite Planting Ongoing

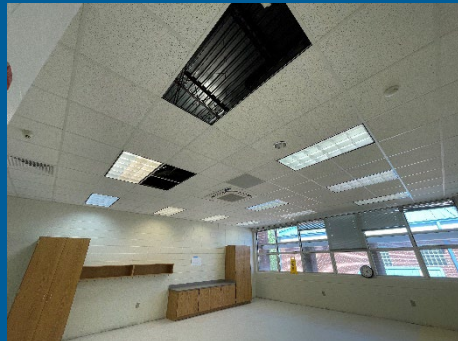

Ceiling Tile Installation in Classroom
Ongoing

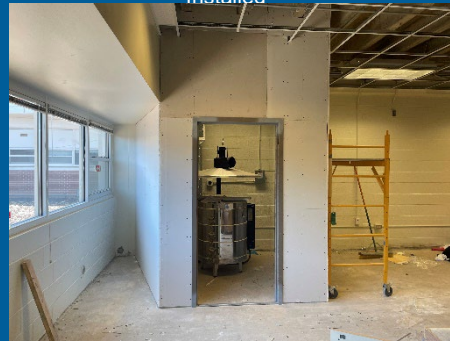

Kiln Room Closet Installed

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$5,548,213
- Budget Status: Within GMP

