

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Woodson Park Academy & YMCA-ELC
Week Ending: July 24th, 2020

THIS WEEK:


- Brick continues at YMCA
 - MEP Overhead continues at WPA
 - Drywall and Finishing continues at WPA
 - Interior Framing and Drywall at YMCA
 - Elevator at WPA
 - Epoxy Floors at WPA
 - Metal Panel install
 - COA inspections – delays occurring due to COVID-19 action
-



Framing at the YMCA



East Elevation at WPA

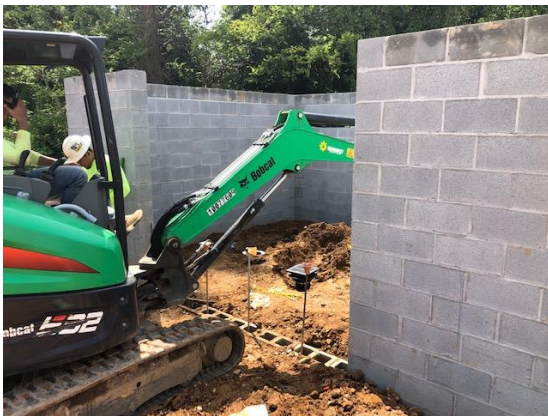

Dumpster Enclosure at the YMCA



Brick at the YMCA



CARROLL DANIEL
CONSTRUCTION

Woodson Park Academy & YMCA-ELC
Weekly Construction Progress Report

WEEKLY CONSTRUCTION PROGRESS REPORT



Monumental Stairs at WPA



Site steps on South side of WPA

NEXT WEEK – July 27th thru July 31st:

- Brick at YMCA
- MEP Overhead continues
- Framing continues
- Metal Panel install continues
- Epoxy Floors continue
- Storefront Frames and Glass at WPA
- Interior Framing and Drywall at the YMCA
- COA inspections – delays occurring due to COVID-19 action

PAYMENT STATUS:

- Gmp#1 \$3,703,488.00
 - Paid to date amount \$2,616,349.45
- GMP#2 \$27,034,273.00
 - Paid to date amount \$13,680,201.15
- GMP#3 \$5,877,688.00
 - Paid to date amount \$1,315,528.70
- GMP#4 \$1,974,712.00
 - Paid to date amount \$140,303.57

WEATHER:

- Total of 1/2" of rain for the week

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- WPA – November 4, 2020
- YMCA-ELC - November 27, 2020

PREPARED BY: Matt Dauber, Carroll Daniel Construction Co.



Woodson Park Academy & YMCA-ELC
Weekly Construction Progress Report
