

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Woodson Park Academy & YMCA-ELC
Week Ending: September 11th, 2020

THIS WEEK:

- MEP Overhead continues at WPA & YMCA
 - Drywall and Finishing continues at WPA
 - Metal Panel install
 - Dryfall paint at the YMCA
 - Tile continues at WPA & YMCA
 - Brick continues at YMCA
 - MEP Trim on Main, 2nd and 3rd levels
 - Ceiling tile install on Main level at WPA
 - Glazing install continues at WPA
 - 3rd floor ceiling grid install at WPA
 - COA inspections – delays occurring due to COVID-19 action
-



Cedar T&G at overhangs on YMCA



Ceiling Grid and Tile at the YMCA




WEEKLY CONSTRUCTION PROGRESS REPORT



Tectum panels at the YMCA



Classroom at the YMCA

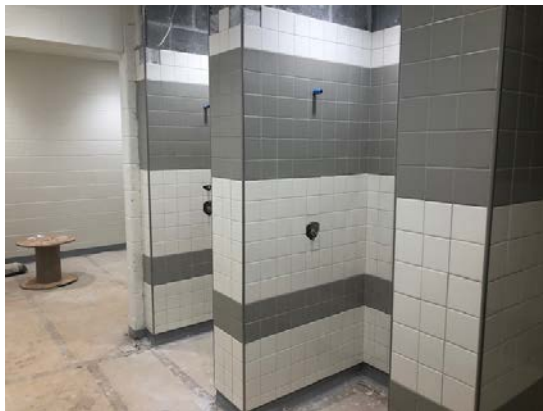

Shower tile at WPA



Outdoor condensing unit install at WPA

NEXT WEEK – September 14th thru September 18th:

- 3rd floor ceiling grid install continues at WPA
- Prime paint at the YMCA
- Tile continues at WPA
- Metal Panel install continues
- Tile installation at YMCA
- MEP trim at 2nd and 3rd levels continue
- Glazing at WPA continues
- COA inspections – delays occurring due to COVID-19 action
- GDOT Permit still not approved



WEEKLY CONSTRUCTION PROGRESS REPORT

PAYMENT STATUS:

- Gmp#1 \$3,703,488.00
 - Paid to date amount \$2,973,648.37
- GMP#2 \$27,034,273.00
 - Paid to date amount \$19,275,272.78
- GMP#3 \$5,877,688.00
 - Paid to date amount \$2,038,955.34
- GMP#4 \$1,974,712.00
 - Paid to date amount \$140,303.57

WEATHER:

- Total of 1" of rain for the week

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- WPA – November 4, 2020
- YMCA-ELC - November 27, 2020

PREPARED BY:

- Matt Dauber, Carroll Daniel Construction Co.

