

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Woodson Park Academy & YMCA-ELC
Week Ending: September 4th, 2020

THIS WEEK:


- MEP Overhead continues at WPA & YMCA
- Drywall and Finishing continues at WPA
- Metal Panel install
- Tile continues at WPA & YMCA
- MEP Trim on LL, Main and 2nd levels
- Brick Continues at YMCA
- Ceiling tile install on Lower Level at WPA
- Glazing install continues at WPA
- 3rd floor ceiling grid install at WPA
- COA inspections – delays occurring due to COVID-19 action



Gas piping on WPA Roof



LL Gang bathroom tile at WPA

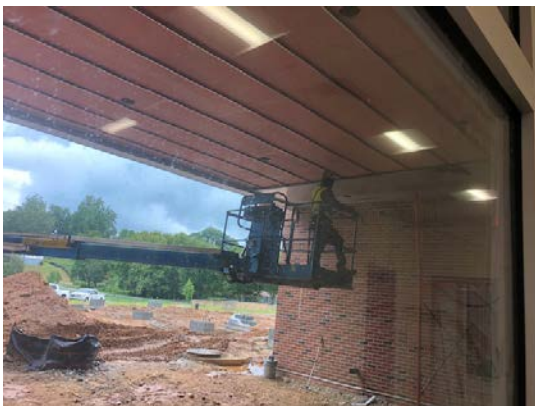

ACM Soffit Panels under Media Center



Commons area at YMCA



WEEKLY CONSTRUCTION PROGRESS REPORT



South Elevation at the YMCA



Interior Brick at circular Windows

NEXT WEEK – September 7th thru September 11th:

- 3rd floor ceiling grid install continues at WPA
- Kitchen equipment installation at WPA
- Tile continues at WPA
- Metal Panel install continues
- Tile installation at YMCA
- MEP trim at main and 2nd levels continue
- Glazing at WPA continues
- Interior paint to begin at YMCA
- COA inspections – delays occurring due to COVID-19 action
- GDOT Permit still not approved
- Water Permit still not approved.

PAYMENT STATUS:

- Gmp#1 \$3,703,488.00
 - Paid to date amount \$2,973,648.37
- GMP#2 \$27,034,273.00
 - Paid to date amount \$19,275,272.78
- GMP#3 \$5,877,688.00
 - Paid to date amount \$2,038,955.34
- GMP#4 \$1,974,712.00
 - Paid to date amount \$140,303.57

WEATHER:

- Total of 1" of rain for the week

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- WPA – November 4, 2020
- YMCA-ELC - November 27, 2020

PREPARED BY:

- Matt Dauber, Carroll Daniel Construction Co.

