



Description

Washington HS - Install Underbleacher Drainage

Taken Date

03/20/2025 at 10:38 am

Uploaded By

Connor Post

Upload Date

03/20/2025 at 10:55 am

File Name

FA53406F-391D-40CD-9476-0B3E...

Album

Washington High School

Location

Booker T. Washington HS



Description

Washington HS - Install Pier Footings

Taken Date

03/20/2025 at 10:38 am

Uploaded By

Connor Post

Upload Date

03/20/2025 at 10:55 am

File Name


2187D780-65DA-4F8A-996F-22A...

Album

Washington High School

Location

Booker T. Washington HS

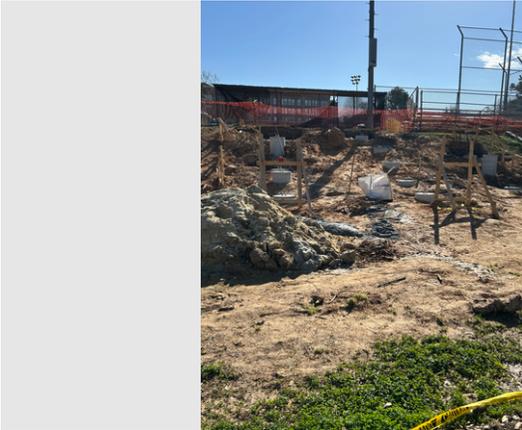

Description

Washington HS - Install Pier Footings

Taken Date

03/20/2025 at 10:37 am

Uploaded By

Connor Post

Upload Date

03/20/2025 at 10:55 am

File Name


4F8C35DA-196C-4C63-A1F2-13A...

Album

Washington High School

Location

Booker T. Washington HS

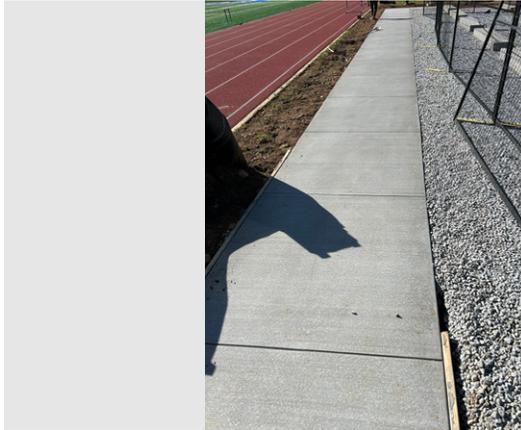

Description

Washington HS - Form and Pour Sidewalks

Taken Date

03/20/2025 at 10:35 am

Uploaded By

Connor Post

Upload Date

03/20/2025 at 10:55 am

File Name

335CB122-20EC-4B39-B659-5BC...

Album

Washington High School

Location

Booker T. Washington HS



Description
 Washington HS - Additional Unforeseen Concrete Foundations

Taken Date
 03/18/2025 at 04:27 pm

Uploaded By
 Craig Bonfig

Upload Date
 03/18/2025 at 04:28 pm

File Name
[4862301D-6FDE-45A1-A21D-BBC...](#)

Album
 Washington High School



Description
 Washington HS - Continue Infiltration Trench Installation

Taken Date
 03/18/2025 at 03:01 pm

Uploaded By
 Craig Bonfig

Upload Date
 03/18/2025 at 03:01 pm

File Name
[9F2FE1EC-D36F-4BC2-8DED-AFE...](#)

Album
 Washington High School



Description
 Washington HS - Continue Pier Footing Prep

Taken Date
 03/18/2025 at 02:59 pm

Uploaded By
 Craig Bonfig

Upload Date
 03/18/2025 at 02:59 pm

File Name
[1429D1F0-AF96-4AEE-A7A8-FC89...](#)

Album
 Washington High School



Description
 Washington HS - Infiltration Trench and Stone Base

Taken Date
 03/17/2025 at 03:20 pm

Uploaded By
 Craig Bonfig

Upload Date
 03/17/2025 at 03:20 pm

File Name
[2B8F684A-2E5C-411C-9AF4-E087...](#)

Album
 Washington High School

WEEKLY PROGRESS UPDATE REPORT

APS – Athletic Seating Project

3/15/2025 – 03/21/2025



Last Week's Activities:

- Excavate Infiltration Trenches – Washington HS
- Grade and Backfill Grandstand Footings – Washington HS
- Install Under Bleacher Drainage – Washington HS
- Begin Grading and Forming for Sidewalks – Washington HS
- Excavate and Pour Pier Footings for Grandstand Ramps – Washington HS

This Week's Activities:

- Complete Forming and Pouring Pier Footings – Washington HS
- Continue Excavation and Installation of Infiltration Trenches – Washington HS
- Continue Under Bleacher Drainage – Washington HS
- Continue Grading and Forming for Sidewalks – Washington HS
- Begin Pouring Sidewalks – Washington HS

Next Week's Activities:

- Complete Excavation and Installation of Infiltration Trenches – Washington HS
- Complete Under Bleacher Drainage – Washington HS
- Continue Grading and Forming for Sidewalks – Washington HS
- Continue Pouring Sidewalks – Washington HS
- Begin Lighting Installation – Washington HS

<u>Contract and Billings</u>	
Contract	
Current Contract Value	\$12,797,800.00
Billings	
Date Last Billing Submitted	2/13/2024
Total Billed to Date (Including Retainage)	\$1,751,567.84
Date of Last Payment	1/16/2025
Amount Paid to Date	\$931,117.20
Amount Open Receivables (Not Including Retainage)	\$584,377.5
Percent Billed to Date	13.69%
