

WEEKLY PHOTO REPORT
APS Field House – Mays High School
May 13, 2022



Prepared For: Atlanta Public Schools


Prepared By: Tyler Cade



Electrical Underslab Rough In



Silt Fence Repair

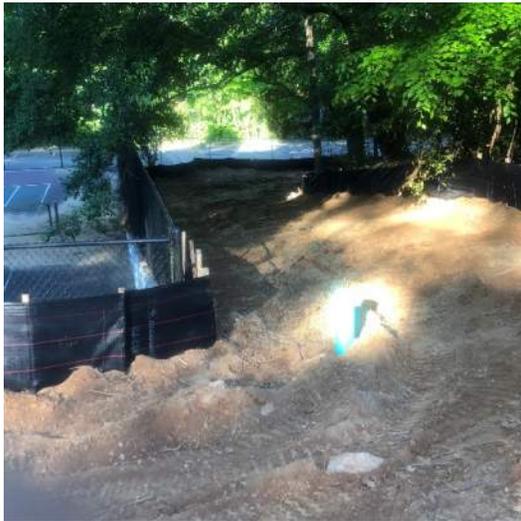

Silt Fence Repair



Plumbing Underslab Rough-In

WEEKLY PHOTO REPORT

APS Field House – Mays High School



May 13, 2022

Last Week's Activities:

- Completed clearing and grubbing
- Completed subgrade undercut backfill
- Continued temporary utilities
- Continued underground utilities
- Continued building pad structural fill
- Continued subbase inspections

This Week's Activities:

- Completed building pad structural fill
- Completed subbase inspections
- Continued temporary utilities
- Continued underground utilities
- Started MEP slab rough in
- Started plumbing slab inspections

Next Week's Activities:

- Continue temporary utilities
- Continue underground utilities
- Continue MEP slab rough in
- Continue plumbing slab inspections
- Start masonry mock-up panels
- Start footing excavations
- Start footing concrete pours
- Start slab on grade prep
- Start slab on grade concrete pours

Contract & Billings	
Contract	
Current Contract Value	\$1,392,366
Billings	
Date Last Billing Submitted	5/10/2022
Total Billed to Date (Including Retainage)	\$150,805
Date of Last Payment	N/A
Amount Paid to Date	\$0
Amount Open Receivables (Not Including Retainage)	\$135,724.50
Percent Billed to Date	11%
