

WEEKLY PHOTO REPORT
APS Field House – Therrell High School
June 17, 2022



Prepared For: Atlanta Public Schools

Prepared By: Morgan Willis




South Corner Footing Rebar



South Opening Footing Rebar



Southeast Footing Rebar

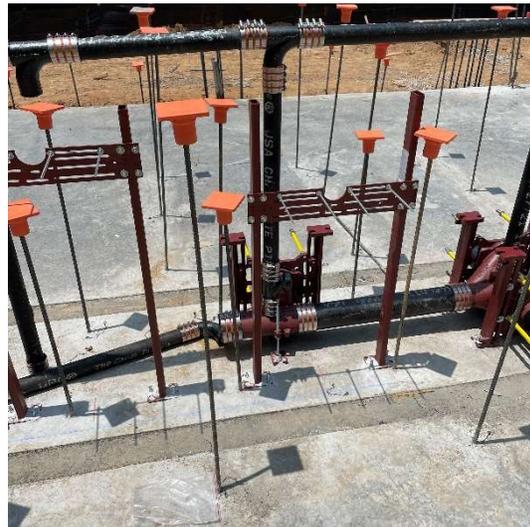

Carrier And Sanitary Install

WEEKLY PHOTO REPORT

APS Field House – Therrell High School



June 17, 2022

Last Week's Activities:

- Continued footing excavations
- Continued footing inspections
- Continued footing concrete pours
- Continued slab on grade prep
- Continued slab inspections
- Continued slab on grade concrete pours
- Continued CMU block installation
- Continued masonry mock-up panels
- Started masonry special inspections

This Week's Activities:

- Completed footing excavations
- Continued footing inspections
- Continued footing concrete pours
- Continued slab on grade prep
- Continued slab inspections
- Continued slab on grade concrete pours
- Continued CMU block installation
- Continued masonry mock-up panels
- Continued masonry special inspections

Next Week's Activities:

- Complete footing inspections
- Complete footing concrete pours
- Complete slab on grade prep
- Complete slab inspections
- Complete slab on grade concrete pours
- Continue CMU block installation
- Continue masonry mock-up panels
- Continue masonry special inspections
- Start dampproofing exterior CMU walls
- Start structural steel installation

Contract & Billings	
Contract	
Current Contract Value	\$1,477,751
Billings	
Date Last Billing Submitted	5/10/2022
Total Billed to Date (Including Retainage)	\$107,692.23
Date of Last Payment	N/A
Amount Paid to Date	\$0
Amount Open Receivables (Not Including Retainage)	\$96,923.01
Percent Billed to Date	7%
