

WEEKLY PHOTO REPORT
APS Field House – Washington High School
June 10, 2022



Prepared For: Atlanta Public Schools

Prepared By: Morgan Willis




Interior 6" Chase Wall



Mechanical Room 8" CMU



Storage Room 8" CMU

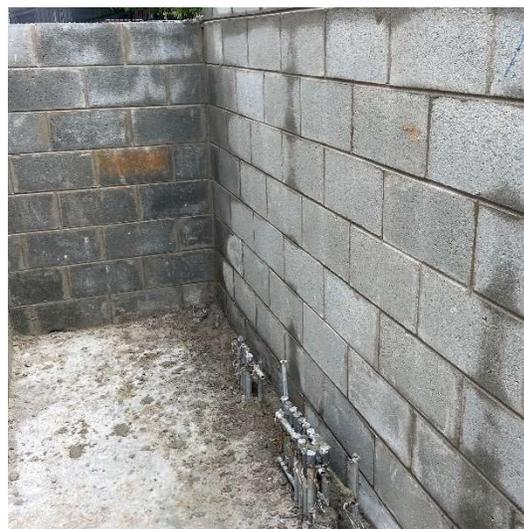

Electrical Room Rough-In

WEEKLY PHOTO REPORT

APS Field House – Washington High School



June 10, 2022

Last Week's Activities:

- Completed MEP slab rough in
- Completed plumbing slab inspections
- Continued footing excavations
- Continued footing inspections
- Continued footing concrete pours
- Continued slab on grade prep
- Continued slab inspections
- Continued slab on grade concrete pours
- Started CMU block installation
- Started masonry mock-up panels

This Week's Activities:

- Continued footing excavations
- Continued footing inspections
- Continued footing concrete pours
- Continued slab on grade prep
- Continued slab inspections
- Continued slab on grade concrete pours
- Continued CMU block installation
- Continued masonry mock-up panels
- Started masonry special inspections

Next Week's Activities:

- Complete footing excavations
- Complete footing inspections
- Continue footing concrete pours
- Continue slab on grade prep
- Continue slab inspections
- Continue slab on grade concrete pours
- Continue CMU block installation
- Continue masonry mock-up panels
- Continue masonry special inspections

Contract & Billings	
Contract	
Current Contract Value	\$1,519,162
Billings	
Date Last Billing Submitted	5/10/2022
Total Billed to Date (Including Retainage)	\$153,410.50
Date of Last Payment	N/A
Amount Paid to Date	\$0
Amount Open Receivables (Not Including Retainage)	\$138,069.45
Percent Billed to Date	11%
