

Ongoing Activities

01/07/19 – 01/11/19

- Erecting sequence 3 steel
- Installing sequence 2 decking
- Setting lower level roof HVAC curbs
- Framing lower level parapet
- Installing lower level interior/exterior block walls
- Installing lower level overhead MEP

Upcoming Activities

- Complete exterior skin mock up
- Continue erecting sequence 3 steel
- Commence erecting sequence 4 steel
- Continue lower level block walls
- Commence installing lower level roofing
- Commence installing fluid applied air barrier

Financial & Schedule Status

Current GMP = \$27.6M
Bill to Date = \$7,897,109

Start Date: July 2, 2018
Current Completion Date:
July 10, 2019

Project Overview



Photo of the project site from west looking at 3rd level steel topping out

Safety Sector



← Correct



Incorrect →

“CMU block handling”


CMU block should be staged as close to the work area as possible to limit travel distance. Inexperienced employees should only carry 1 block per hand; experienced employees can carry 2 blocks per hand (see pictures at left for correct and incorrect methods).



Third level roof bar joists going in



West and South lower level CMU walls topped out

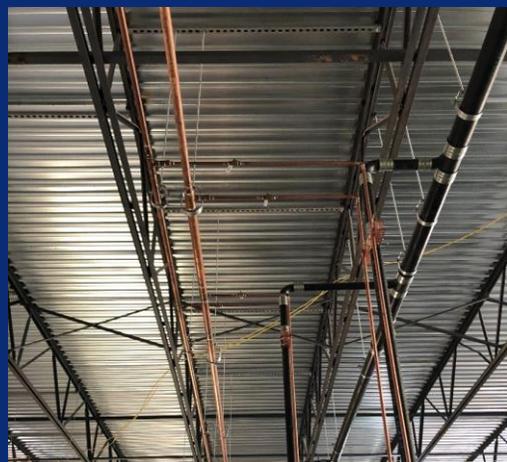

Lower level O/H plumbing lines installed



Lower level roofing material being delivered
