

Ongoing Activities

01/14/19 – 01/18/19

- Erecting sequence 4 & 5 steel
- Installing sequence 3 decking
- Installing lower level HVAC blockouts
- Framing lower level parapet and exterior walls
- Installing lower level interior/exterior block walls
- Installing main level overhead MEP
- Installing lower level roof

Upcoming Activities

- 2nd level west elevated slab pour
- Continue erecting sequence 4 & 5 steel
- Continue lower level block walls
- Continue installing lower level roofing
- Topping out celebration

Financial & Schedule Status

Current GMP = \$27.6M
Bill to Date = \$7,897,109


Start Date: July 2, 2018
Current Completion Date:
July 10, 2019

Project Overview



Photo of the project site from Westhaven looking south

Safety Sector

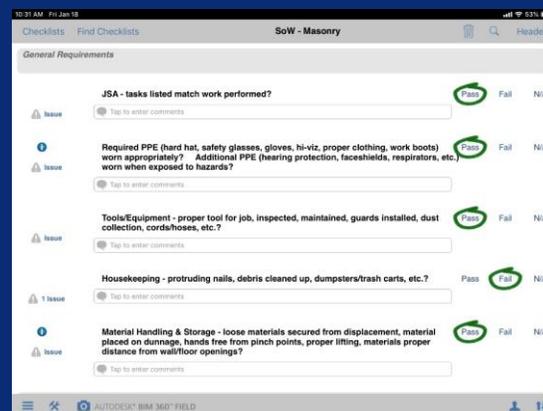

“Safety Walks”

In accordance with JE Dunn’s Safety and Accountability Matrix, team members should conduct daily and weekly safety walks. These walks should be documented in BIM 360 Field (screenshot to left) to ensure all parties are aware of successes and shortfalls.

Fluid applied air barrier installed



Exterior framing starting



Lower Level roof install ongoing



Stage area in lower level



East section (seq 4 steel) viewed from lower level roof
