

## Ongoing Activities

4/29/19 – 5/03/19

- Metal panel installation on elevation F-1
- Prime paint and ceiling grid on main east
- Final roof layer on roof 4
- 1<sup>st</sup> coat finish painting walls on lower level
- Dumpster enclosure wall ongoing
- Brick install on elevation K
- Polished block install on walls at terrace
- Ceramic tile install in lower level gang restrooms
- 1<sup>st</sup> coat prime painting on main east

## Upcoming Activities

- Elevator install
- ERU system start-up (5/06/19)
- Finish walls / prime paint 2<sup>nd</sup> level east
- Overhead door install at second level east
- Commence epoxy flooring in gang restrooms
- Commence VCT install

## Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$20,367,027

Current Completion Date:  
July 10, 2019

## Project Overview



View of project site east looking west at site of future playfield

## Safety Sector



## Electrical Room Controlled Access

Conspicuous signs must be posted at the entrances to electrical rooms and similarly guarded locations to alert people to the electrical hazard and restrict entry to unauthorized people. Here the electrician has posted appropriate signage and keeps doors locked when unoccupied.



Dumpster enclosure in progress



VRV refrigerant lines run and pressure testing in progress




Brick topped out on Elevation J in vicinity of South Stairs



Storefront and curtainwall in progress on west stair



Roof 4 final layers complete (over media center)

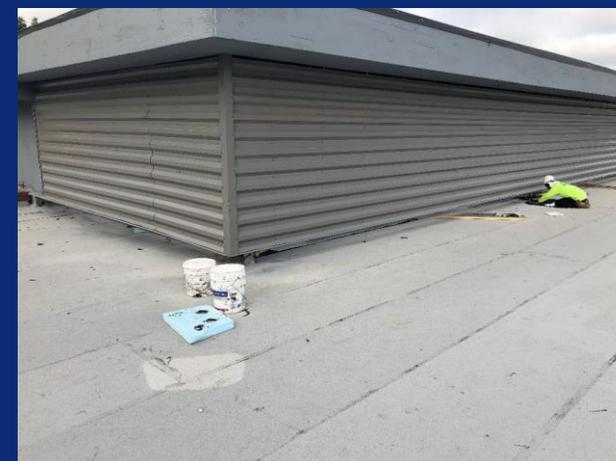

Mechanical screenwall enclosure metal panels in progress



2<sup>nd</sup> floor east topped out (Band Rm 373)



Ceramic tile and lavatories installed in lower level gang restrooms



First coat finish accent paint in gymnasium



Dryfall and permanent lighting in progress over C1-1 stairs



Prime paint and grid installed through main east (Kindergarten Rm 276)



ACT cloud grid installed in media center
