

Ongoing Activities

05/06/19 - 05/10/19

- Metal panel installation on elevation G-1 and L
- Finishing walls on 2nd east
- ERU and VRF start-up
- Hardscape install near playground and Elev. H
- Dumpster enclosure wall ongoing
- Brick install on elevation K
- Install exterior hollow metal doors
- Ceramic tile install in main level gang and single restrooms
- Elevator shaft framing
- Epoxy flooring in lower level gang restroom

Upcoming Activities

- Elevator install
- ERU and VRF system start-up on east
- Prime paint 2nd level east
- Overhead door install at second level east
- Commence VCT/carpet install
- Millwork delivery

Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$20,367,027

Current Completion Date:
July 10, 2019

Project Overview



View of project site from north looking south

Safety Sector



Safety Week 2019

Safety week 2019 is in full swing this week. JE Dunn utilizes the Safety Spotlight and Incident Broadcasts to provide real examples of what can happen on our jobs, and how to avoid them in the future. Access to this information is available on the JE Dunn Connect page.

-Dan Kaufman, East Region President



Brick nearing completion at Elevation K (exterior of gang restrooms)



Hardscape in progress at playground and end of east wing



Painting in progress at terrace



Exterior hollow metal doors installed



Metal panel install in progress on Elevation G-1 (2nd east labs)



Storefront system installed at gymnasium entrance



Permanent lights installed and burning on main west (Inter. Offices 205)



Grid installed and air distribution in progress on 3rd level




Elevator shaft install in progress



Fixtures prepped and staged for install on 3rd level



Finishing walls at 2nd east (Band Rm 373)

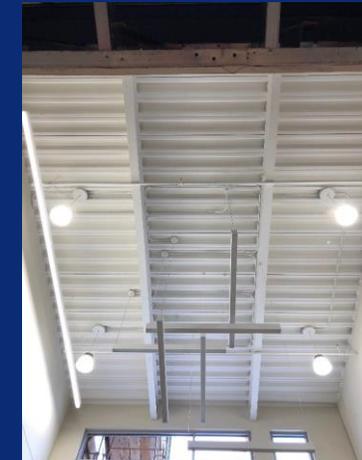

Lighting installed and burning over gymnasium stairs
