

## Ongoing Activities

05/13/19 - 05/17/19

- Metal panel installation on elevation G-1 and I
- Finishing walls on 2<sup>nd</sup> east
- Hardscape install near playground and Elev. H
- Install interior doors on lower level and main West
- Ceramic tile install in second level gang
- Elevator shaft framing
- Epoxy flooring in lower level gang restroom
- Pouring hardscape in playground area
- Overhead door install at second level east
- Received ceiling cover for Second floor West on 5/16/19

## Upcoming Activities

- Elevator install
- ERU and VRF system start-up on east
- Prime paint 2<sup>nd</sup> level east
- Commence VCT/carpet install
- Install doors on second West

## Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$20,367,027

Current Completion Date:  
July 10, 2019

## Project Overview



View of project from East looking West

## Safety Sector



## Warning lines


Warning lines are required as a measure for fall protection. Here we have placed warning lines around the perimeter of all roofs to ensure all personnel are aware of the hazard and requirement to tie off.



Walk pads on roof 1 & 2



Metal panel insulation in progress on elevation 1

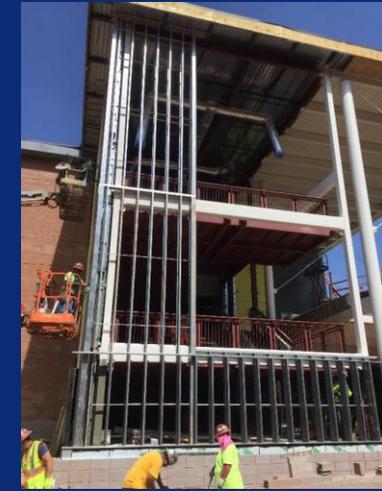

South stair framing in progress



Store front doors and windows installed at East stair



Sheathing in progress at South stair



Dumpster pad brick complete and slab poured



Interior doors installed at gymnasium entrance



Mill work delivered and awaiting install



First coat finish paint in principal's conference room



Overhead door installed in STEM lab



Epoxy flooring complete in lower level restrooms



Ceramic tile in progress in main level restrooms
