

Ongoing Activities

05/20/19 - 05/24/19

- Playground Installation
- Finishing walls on 2nd east
- Main level south terrace hardscapes
- Elevator installation
- Ceramic tile install in third level gang
- Epoxy flooring in main level gang restroom
- Grading for playfield and south playground
- Brick cleaning on all elevations
- Dryfall paint on ceilings at second level
- Metal panel install at elevation I and L

Upcoming Activities

- Gymnasium Floor Installation
- South stair tower curtain wall
- South playground
- Commence VCT/carpet install
- Millwork installation

Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$20,367,027

Current Completion Date:

July 10, 2019

Project Overview



Aerial view of project from Northside

Safety Sector



Elevator Hoistway Protection

The greatest hazard associated with elevator installation is falls of personnel, materials, and equipment. JE Dunn installed physical controls on every elevator access point and enforced no materials being stored within 6 feet of the elevator shaft opening.



North Playground Installation in Progress



Stairs and Sidewalk Hardscapes at East-Side Terrace



Hardscapes South Playground



Grading Outside East Wing Stair in Preparation for Northeast Concrete Stair Install



East Wing Metal Paneling in Progress




North Entrance Seat Wall CMU Installation



Elevator Installation



Kitchen Equipment and Prep for Ceiling installation

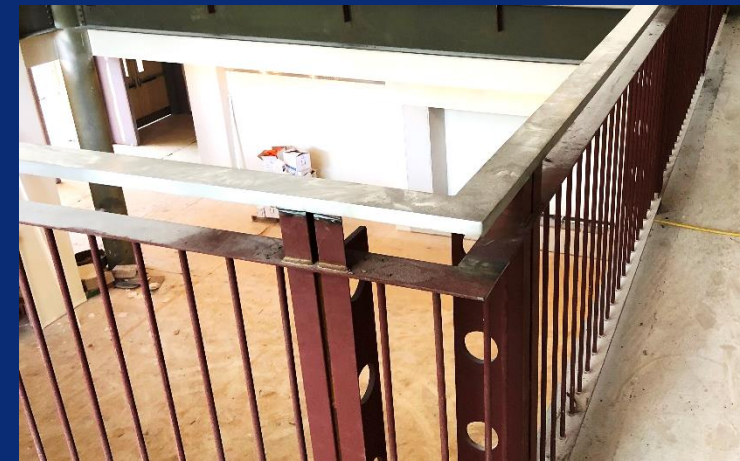

Stainless Steel Handrail installed



Toilet Partitions Installed Lower Level Restrooms



Dryfall Installation and Paint Ongoing on Middle Section 2nd level



First coat final Paint 2nd floor classrooms
