

## Ongoing Activities

9/10/18 – 9/14/18

- Site grading and balancing in progress
- Storm drainage piping installation in progress
- East side underground detention system excavation and installation in progress
- Fire line site utility installation ongoing
- Layout in progress for building foundations

## Upcoming Activities

- Curb, gutter and binder coarse for the parking lot and Richland cut through
- Retaining wall and foundations at the lower level

## Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$2,015,811

Current Completion Date:

July 10, 2019

## Project Overview



View of Project Site from Richland Road

## Safety Sector



## Hand-Held Power Saw Safety


When using a hand-held power saw, workers wear a face shield to protect from potentially harmful debris while operating the tool. This face shield is worn in addition to all other required PPE.



Fire Line Installation



East Side Detention System Installation  
and Backfill

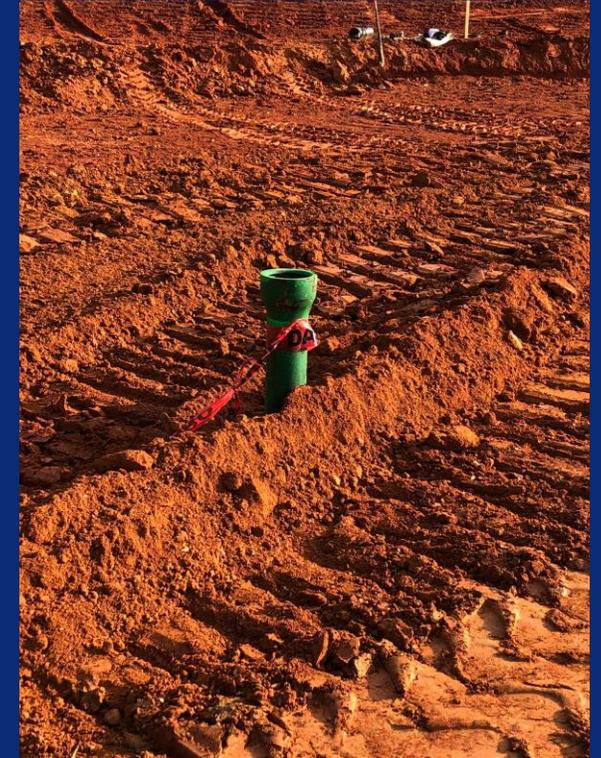

Sanitary Utility Line Installation
