

Ongoing Activities

10/29/2018 – 11/02/2018

- Lower level foundation rebar installation
- Complete foundations and walls at lower level
- Below grade waterproofing on retaining wall
- Foundation block at lower level
- Kitchen piping underground install and inspection
- Install stone for lower level slab-on-grade
- Completed pull-plan for interior rough-in

Upcoming Activities

- Continue waterproofing walls at lower level
- Continue foundation block at lower level retaining wall
- Continue backfilling at lower level retaining wall
- Main level foundations
- Lower level slab-on-grade pour

Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$2,783,384

Current Completion Date:

July 10, 2019

Project Overview




Photo of the project site from newly leveled main floor looking South

Safety Sector



“First Move Forward”

JE Dunn implements the “First Move Forward” initiative on all jobsites. The intent is that reversing in to parking spaces ensures all team members can see what is in front of them and where they are going when they leave the job site.

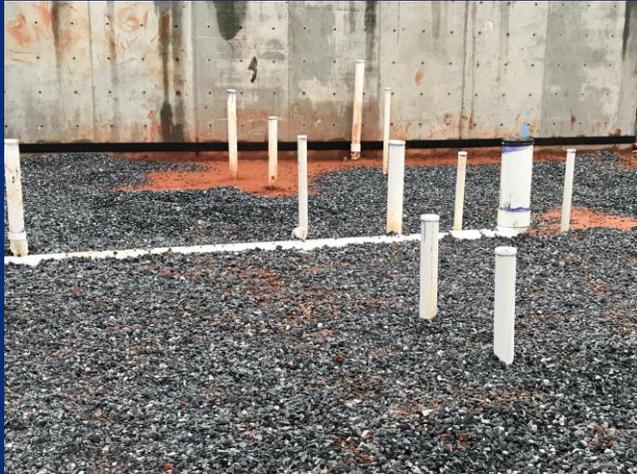

Lower level gang restroom underground plumbing



Interior rough-in pull plan



Balancing the main level pad



Kitchen underground piping



Prep for SOG in gymnasium
