

Ongoing Activities

11/5/18 – 11/9/18

- Below grade waterproofing on retaining wall
- Lower level underground electrical rough-in
- Completion of stone installation for lower level slab-on-grade
- Poured west braced frame footings on main level
- Layout and installation of rebar for main level footings

Upcoming Activities

- Lower level slab on grade pour
- Continue waterproofing walls at lower level
- Continue backfilling at lower level retaining wall
- Continue main level foundations
- Commence main level underground MEP

Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$3,690,041

Current Completion Date:

July 10, 2019

Project Overview



Photo of the project site from main level looking South

Safety Sector




“Safety Cables”

Perimeter safety cables are required on any multi-story structures. JE Dunn keeps the necessary materials on hand to install, ensuring the safety of all team members.



Lower level prep for SOG

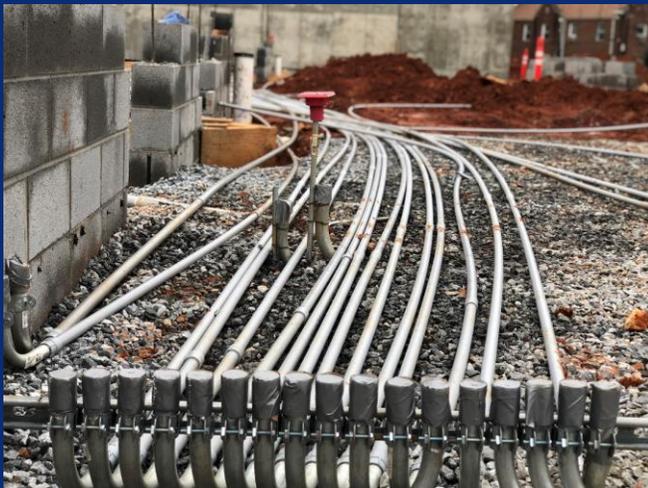

Lower level underground electrical rough-in



Concrete truck convoy on site for braced frame foundations



Braced frame foundation being poured
