

Ongoing Activities

12/10/18 – 12/14/18

- Poured main level west slab on grade
- Erecting sequence 1 & 2 steel
- Main level east underground MEP
- Constructing exterior skin mock up
- Pouring main level east braced frame footings
- Main level east slab on grade prep

Upcoming Activities

- Main level east slab on grade pour
- Complete exterior skin mock up
- Continue main level east underground MEP
- Commence erecting sequence 3 steel
- Continue lower level block walls

Financial & Schedule Status

Current GMP = \$27.6M

Bill to Date = \$5,197,152

Start Date: July 2, 2018

Current Completion Date:
July 10, 2019

Project Overview




Photo of the project site with simultaneous concrete pour and steel install

Safety Sector



“Silica Exposure”

OSHA standards require controls to minimize exposure to silica dust be implemented any time concrete/masonry/stone cutting takes place. Finishing trade partners utilized a mixture of wet cutting and vacuum attachments to control the resulting dust during slab cutting.

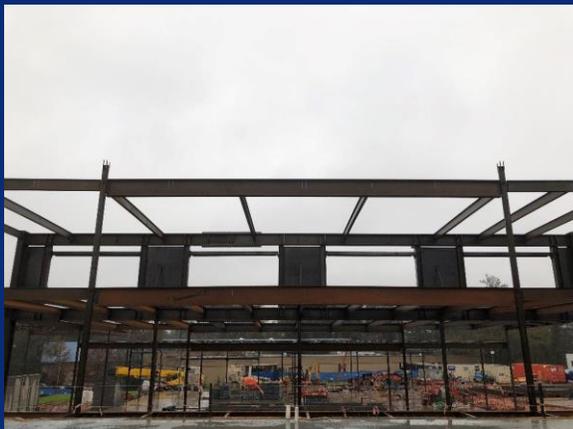

Transfer truss spanning gym installed



Bar joists installed over cafeteria



Iron workers installing sequence 1 & 2 steel



Main level west slab on grade poured



Sanitary lines for main level east installed
