


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 10/06/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

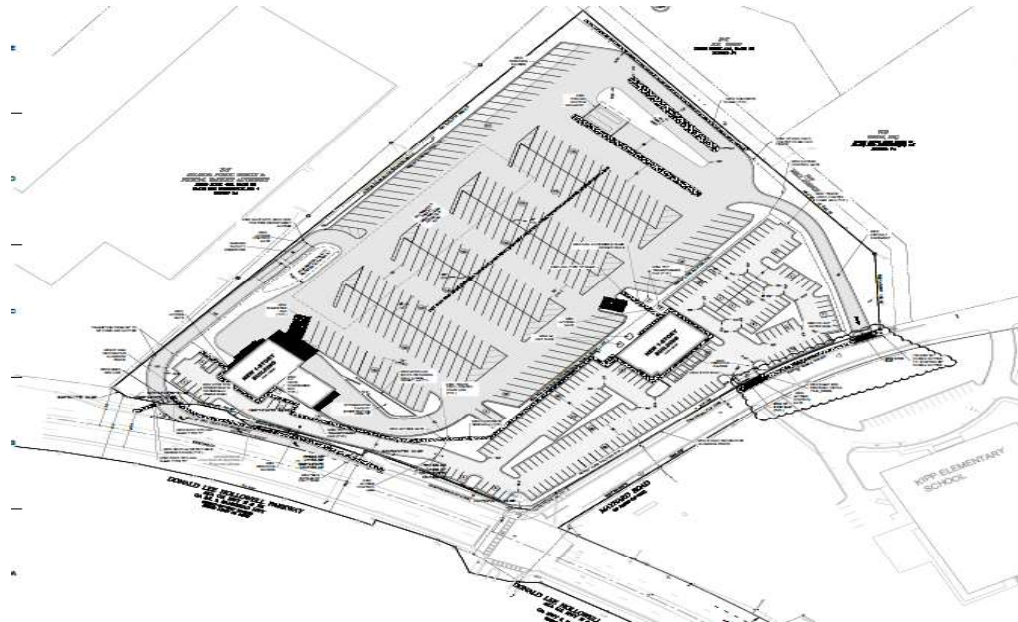

Construction Activities this week

- CLEARING/GRUBBING AND DEFORESTATION OF THE PROJECT JOBSITE
- TRAVIS PRUITT & ASSOCIATES, INC COMPLETED THE 7-DAY INITIAL EROSION CONTROL INSPECTION
- MOBILIZED SITE CLEARING EQUIPMENT TO THE SITE
- RECEIVED DELIVERY OF JOB TRAILER OFFICE EQUIPMENT

CONSTRUCTION ACTIVITIES PLANNED NEXT WEEK

- CONTINUE WITH MEP & UTILITY COORDINATION
- CONTINUE WITH SITE CLEARING AND GRUBBING
- COMPLETE SETUP OF JOBSITE TRAILER (I.E. POWER/WATER/INTERNET)

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

