

Ongoing Activities

4/8/19 – 4/12/19

- LL ceiling and east wall cover inspection: 4/10/19
- Ceiling grid install on main west
- Two-siding walls on 2nd level west
- Metal panel installation on elevation F
- Interior insulation install on east
- Final roof layer on roof 3
- Finishing / priming main level west
- Polished block install at lower level ramp walkway
- Brick install on elevation G and C-1
- Site work and cast in place walls at terrace

Upcoming Activities

- Cover up hard ceilings on lower level
- Continue 1st two layers of all roofing
- Main west ceiling cover up inspection (4/25/19)
- 1st coat painting on 3rd level
- Overhead door install at second level east
- Third floor drywall install
- VRF condenser unit delivery and install

Financial & Schedule Status

Current GMP = \$27.6M

Start Date: July 2, 2018

Bill to Date = \$16,300,269

Current Completion Date:


July 10, 2019

Project Overview



View of project looking south, from Westhaven

Safety Sector

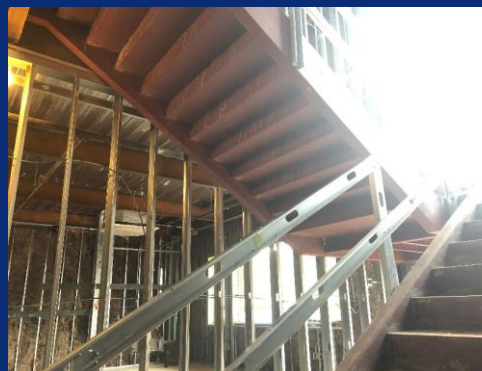

Temporary Handrails

Stairway handrails (30"-37" above tread) must be provided on all open sides of stairs with 4 or more risers or rising more than 30 inches, whichever is less. Temporary rails (cold formed steel framing) were added here ahead of permanent rails being installed.



Whitecap roof in progress over 3rd level



ACMU install at south entry stairs and planter wall



View from east end, looking west



Metal Panel Install at North Entrance
(Elevation F)



Mod block wall A installed at east end



Brick installed on elevation G



2nd siding and finishing on second level west (rm 313)




3rd level gang restroom chase walls installed



First coat of primer in corridor C6-2



Insulation install in progress at main east

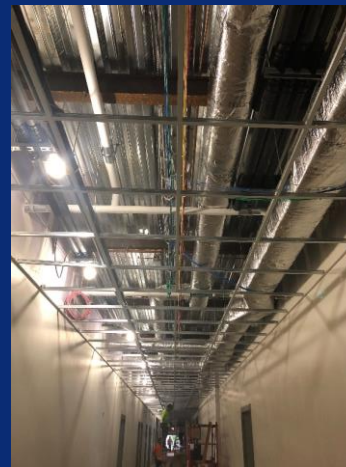

Grid install in progress in corridor C1-2



Panels installed in 2nd level electrical room
