

BENTEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 05/15/2023-05/19/2023



Balfour Beatty

Current Activities 05/15/23-05/19/23


- Installation of electrical shut off switches for VRF system at area D and E.
- Installation of low voltage data drops in Area A,B,C
- Install Lights & low volt in ceiling grid in area A, B, C
- Install Corridor Lights – Ongoing
- Cut Ceiling Tile Border
- Final Coat of Finish Paint and Accent walls in Area B,C - Complete
- Paint Bathroom Ceilings
- Final Coat of Finish Paint remaining Areas
- Install Ceiling Grid in Area E, Kitchen, and Cafeteria - Complete
- Install Ceiling Tile Area C - Complete
- VCT Flooring Install Area D
- Install Light fixtures and devices in Area E
- Area A Ceiling Tile install - Complete
- Cleaning for upcoming wax
- Vacuum VRF systems
- Area B,C ceiling tile instal

Upcoming Activities 05/22/23-05/26/23

- LED Monument Sign install
- Area A Ceiling Tile install
- First Coats of Wax in Classrooms
- Cafeteria Ceiling Tile Install
- Area E VCT Flooring Install
- Crane pick For HVAC units



Library Ceiling Tile and Flooring Installed

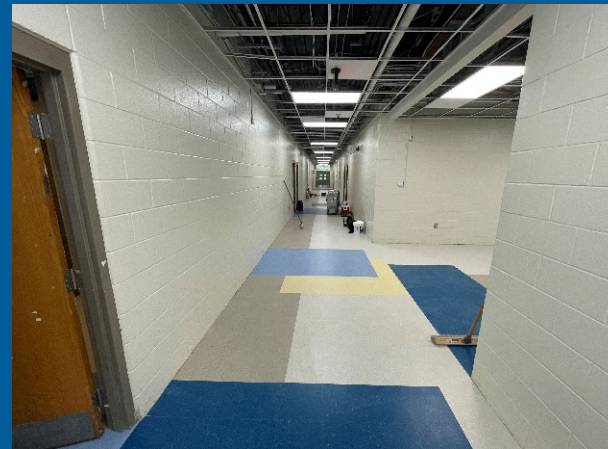

Corridor Flooring install currently ongoing throughout building

Progress Photos



New Generator Concrete Pad Poured



Principal office being prepped and primed
for first coat of finish paint



New offices/conference room ceiling grid
and HVAC components installed

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$5,548,213
- Budget Status: Within GMP



Balfour Beatty
