

CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 10/22/18-10/26/18



The Kindezi School

Balfour Beatty

10/15/18-10/19/18 Activities



- Building survey layout
- Abatement
- Installation of site utilities
- Re-Roofing
- Mobilization and start of retaining wall foundation



Survey Layout and Footing Excavation



Renovation Framing and MEP Rough

Balfour Beatty


10/22/18-10/26/18 Activities



- Prep for hurricane
- Interior MEP rough
- Re-roofing
- Abatement
- Setting of grease traps



Interior MEP Rough and framing at renovation

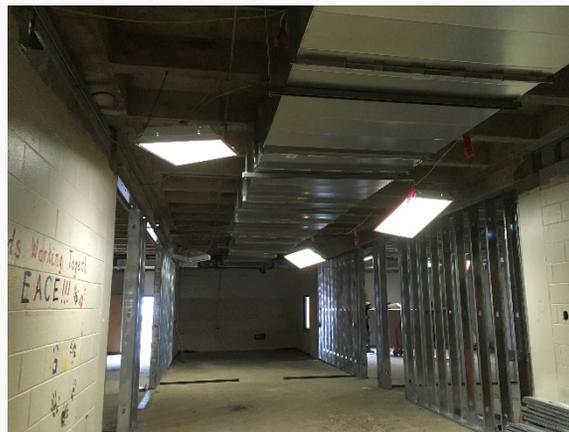

Extension of rubble wall at Mary St

Balfour Beatty

10/22/18-10/26/18 Activities Continued



Excavation and pouring of footings



Installation of wall rebar

Balfour Beatty

10/22/18-10/26/18 Activities Continued



New Building foundations and wall formwork

Balfour Beatty



10/29/18-11/2/18 Activities

- Continue Renovation Rough
- Site Water Lines
- Curb and Gutter
- Rubble Wall at Mary Street
- Retaining Wall and Foundations

Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/26/19 per 10/23/18 schedule update

Project Financials

- Current contract value: \$14,400.00
- Approved OCO 1 \$75,856.45 – Pending execution

Balfour Beatty
