

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 10/28/19-11/1/19



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 10/28/19 - 11/1/19

- Completed final phase of abatement and air sampling at the 2010 building
- Complete the removal of all florescent light fixtures
- Completed structural demo at final abatement area
- Demo of main entry stairway and masonry walls
- Installed the new storm structure at the bus loop
- Demoed sidewalks at 2021 entrance
- Commencement of site grading
- Investigated existing Mechanical, Electrical, and Plumbing systems.
- Demoed all water fountains at 2020 and 2021 buildings

Upcoming Activities 11/4/19 - 11/8/19

- Continue investigating existing Mechanical, Electrical, and Plumbing systems.
- Prep plumbing systems for installation of new fixtures.
- Prep electrical systems for installation of new panels.
- Demo existing monument sign at drive entrance
- Demo sidewalks and planter at front entrance
- Install new gravel access road at the back of the school




Demo of Main Entry Stairway
and Masonry Walls



Controlled Access Zone for Entry Stair Demo

Activities

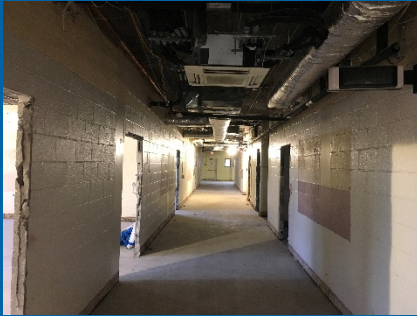


Completed Removal of Light
Fixtures



Restroom Demo at 2010 Building



Demo of Sidewalks at 2021
Building Entrance

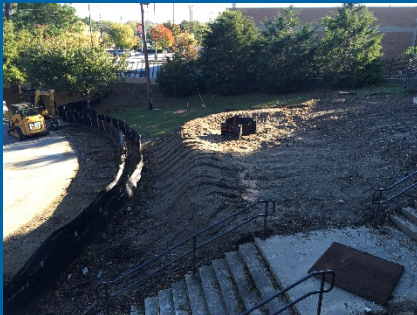

Installed New Storm Structure
at Bus Loop, Silt Fence, and
Site Grading

GMC

Goodwyn, Mills, & Cawood

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 10/22/2019 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$335,416.92
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
