

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 1/6/20-1/10/20



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 1/6/20 - 1/10/20


- Demoing and reinstalling roofing at Building 2010.
- Installing conduit and wall rough-in of new electrical systems.
- Installing overhead rough-in of plumbing systems insulation of pipes.
- Installing condensate drain lines and line sets to FCUs in Building 2010.
- Installing duct work in Building 2010
- Installing lighting in Media Center.

Upcoming Activities 1/13/20 - 1/17/20

- Install masonry walls and masonry wall reinforcement in Building 2020.
- Continue demo and reapplication of roofing.
- Continue installing conduit and wall rough-in of new electrical systems.
- Continue installing duct work and control wire to FCUs.
- COnTinue overhead rough-in of plumbing system.
- Install new drains in courtyard.
- Pour new sidewalks in courtyard.
- Begin fire alarm rough-in.



Install Condensate Drains and Line Sets to FCUs in Building 2010

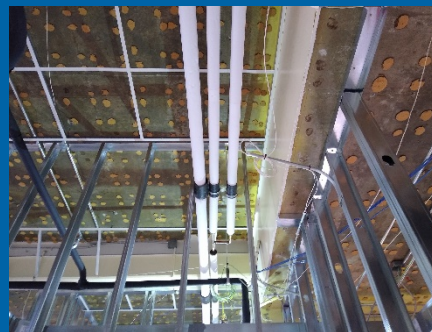

Installation of Overhead Pipes and Pipe Insulation in Building 2010

Activities



Install New Lighting in Media Center



Install Conduit in Classrooms



Continue Demolition and Replacement of Roof



Goodwyn, Mills, & Cawood

Saw Tothing and Removal of CMU in Media Center

Patching of CMU Walls

In-fill of Masonry Walls

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 12/17/2019 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$1,634,547
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
