

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 3/23/20-3/27/20



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 3/23/20 - 3/27/20

- Continuing low voltage and fire alarm rough-in
- Continue installation of new metal roofing
- Continue roof demo and replacement at building 2010
- Pour entry slab and entry retaining wall footings
- Continue backfill at ADA ramp
- Lay VCT at building 2021 & 2020 classrooms
- Finish 1st coat of paint in Gym and STEM Lab
- Install ceiling grid and lights in 2010B corridor
- Install hard ceilings at building 2010
- Install tile in restrooms at building 2021
- Hang sock duct in gym

Upcoming Activities 3/30/20 – 4/3/20

- Continue demo and reapplication of roofing
- Continue low-voltage and fire alarm rough-in and device installation
- Continue canopy footing and retaining wall excavation and concrete pours
- Continue install of VCT at building 2020
- Continue install of tile in restrooms in 2020
- Waterproof entry retaining walls and stairs
- Pour exterior retaining walls at entry
- Install exterior curtain wall system
- Hang lights and acoustic baffles in Gym



Finish 1st Coat of Finish Paint in Gym



Pour entry slab and entry retaining wall footings

Activities



New Standing Seam Metal
Roofing Installation



Lay VCT at Building 2021 &
Building 2020



Install Tile at Building 2021
Restrooms




Goodwyn, Mills, & Cawood



Begin 1st Coat of Finish Paint at
STEM Lab



Hang Ceiling Grid and Lights at
Building 2010A Corridor

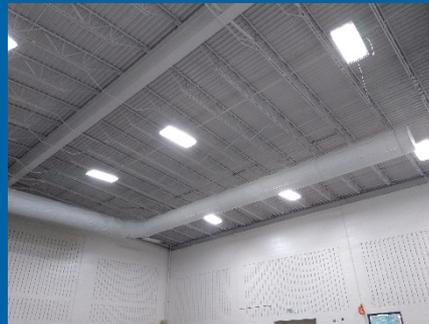

Hang Sock Duct in Gym

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 03/24/2020 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$3,082,225
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
