

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 5/18/20-5/22/20



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 5/18/20 - 5/22/20

- Complete install of canopy at ADA ramp
- Finish pouring Ramp and Sidewalk
- Install accessories in restrooms at building 2010
- Set flagpole and flagpole sleeve
- Finish install of casework in classrooms at building 2010
- Install storefront system and glass at entry
- Continue laying VCT, carpet, and LVT at building 2010
- Begin install of epoxy flooring on connector stairs
- Hang doors in corridors and at exterior of building 2010
- Continue install of handrails at ADA ramp
- Install acoustic baffles in STEM Lab and Gym

Upcoming Activities 5/26/20 – 5/29/20

- Complete install of flooring at building 2010
- Complete install of casework at building 2010
- Complete install of doors at building 2010
- Move APS furniture into building
- Install lights on ADA canopy
- Continue install of low voltage at building 2010
- Pressure wash exterior surfaces
- Install lights at Entry
- Install LED sign at entrance




Set Flagpole and Flagpole Sleeve



Complete Install of Canopy at ADA Ramp &
Finish Ramp and Sidewalk

Activities

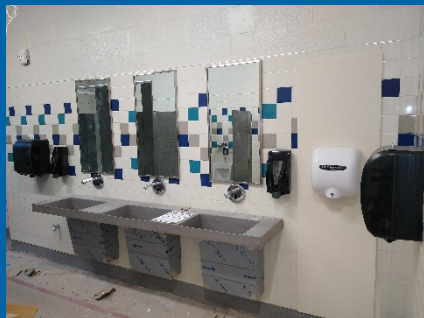

Install Restroom Accessories at
Building 2010



Finish Install of Casework in
Classrooms at Building 2010



Continue Install of VCT at
Building 2010

GMC


Goodwyn, Mills, & Cawood



Install Storefront System and
Glass at Entry



Hang Acoustical Baffles in
STEM Lab

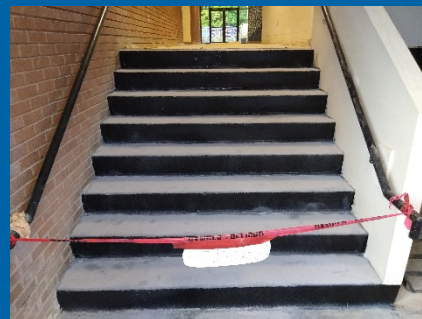

Begin Install Epoxy Treads at
Connector Stairs

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 05/19/2020 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$5,351,169
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
