

JACKSON

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 1/8/2024-1/12/2024



Balfour Beatty

Current Activities 1/8/2024-1/12/2024


- **Complete**
 - Pressure testing of Building 2010 and Building 2011 upper level
 - Hanging FCU Upper Level Building 2010
 - HVAC piping Upper Level Building 2010
- **Started/Ongoing**
 - Electrical tie-in ongoing for mechanical units
 - Electrical rough-in for low voltage
 - Demo of Roofing and begin Reroof
 - HVAC Piping at Principal office
 - Hanging FCU Lower Level Building 2011
 - HVAC Piping Lower Level Building 2011
 - Added Demo of Casework per APS Request

Upcoming Activities 1/15/2024-1/19/2024

- Insulation at HVAC piping
- VRV unit connection and ductwork Building 2010
- Low voltage to begin pulling new wire
- Pour Equipment Pads



**HVAC Rough-in Ongoing
Demo Complete**

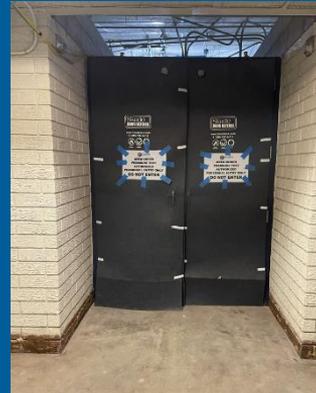

Progress Photos



Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$12,330,741.00 (pending GMP #3 amendment execution)
- Progress Billed to Date: \$2,835,983.77
- Budget Status: Within GMP

