

JACKSON

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 2/5/2024-2/9/2024



Balfour Beatty

Current Activities 2/5/2024-2/9/2024


- Complete
 - Roofing TPO (with the exception of Metal Trimming)
 - Disconnected Cooling Tower
 - Demo of Cooling Tower piping
- Started/Ongoing
 - Electrical tie-in ongoing for mechanical units
 - Electrical installing cable trays
 - Electrical rough-in for low voltage
 - Low Voltage (intercom) wire pulling
 - Insulation at HVAC piping Building 2010
 - Ductwork ongoing at Pods Building 2010
 - HVAC Piping Lower Level Building 2011
 - Insulation at ductwork upper level building 2011

Upcoming Activities 2/12/2024-2/16/2024

- Low voltage (Fire and Data) to begin pulling new wire
- Pour exterior Equipment Pads
- Roofing (Shingles and Metal Trim)
- Abatement at Kitchen
- Demo at Kitchen



Kitchen ready to begin demo
Ductwork ongoing at Pods

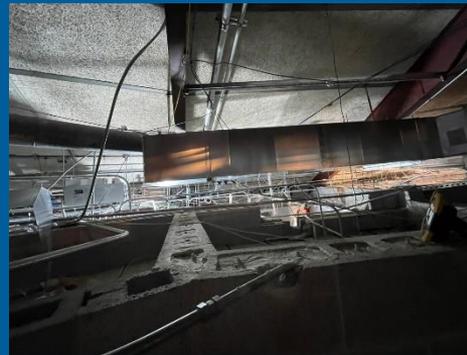

Progress Photos



Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$12,615,400.40
- Progress Billed to Date: \$2,835,983.77
- Budget Status: Within GMP

