

JACKSON

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 11/13/2023-11/17/2023



Balfour Beatty

Current Activities 11/13/2023-11/17/2023

- **Complete**
 - BBC has submitted Revision 7 change order. Pending approval per 11/15 meeting
 - Demo of toilet partitions
- **Started/Ongoing**
 - Demo of hard ceilings at restrooms
 - Demo of carpet at Media Center
 - Electrical rough-in upper level building 2010
 - HVAC rough-in in Mech room
 - Abatement and containment for plumbing lines
 - BBC Pricing Revision 8 Drawings

Upcoming Activities 11/20/2023-11/24/2023



- Demo of HVAC in media center and reloop waterpiping
- HVAC rough-in
- Once abatement is complete – demo plumbing fixtures



**Demolition ongoing
Rough-in Ongoing**



Progress Photos

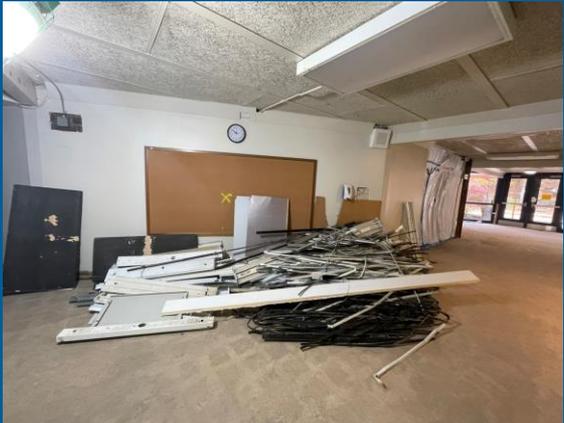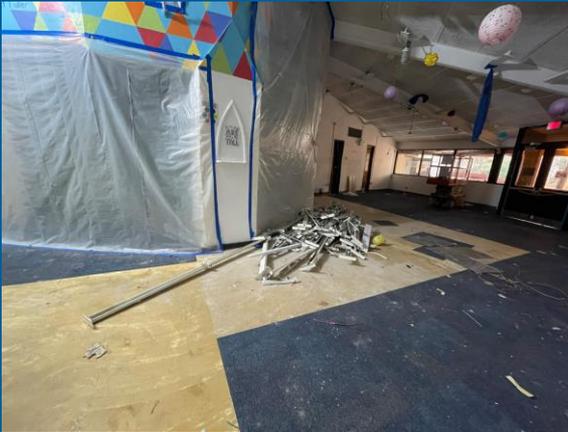

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$1,526,692.67
- Budget Status: Within GMP

