

MILES

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 07/14/2025-7/18/2025




Balfour Beatty

Current Activities 7/14/2025 - 7/18/2025

- Complete
 - Move Management
 - Floor Protection
 - Masonry - Cutting Holes for OFS
- In Progress - Interior
 - Interior Demolition – 80%
 - MEP investigations
 - Duct Cleaning
 - Electrical Reroute
- In Progress - Exterior
 - Roofing Replacement – 80%

Upcoming Activities 7/21/25-7/25/25

- Structural Steel – Support for Rooftop Mech. Units


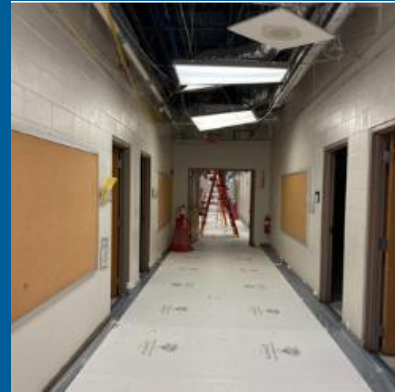


Above Ceiling Demo



Roof Replacement

Progress Photos

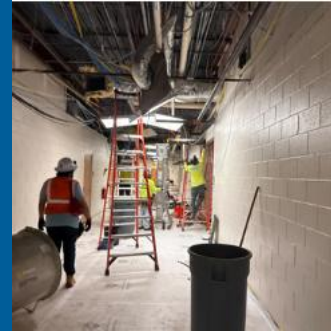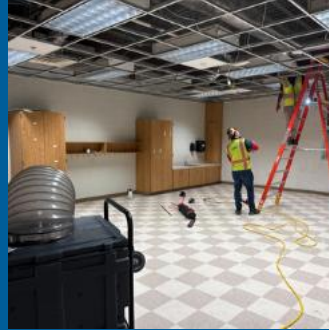

 LORD AECK SARGENT

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$10,528,700.00
- Progress Billed to Date: \$1,630,405.29 = 15% Completion
- Budget Status: Within GMP

