

MILES

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 07/28/2025 - 8/1/2025



Balfour Beatty

Current Activities 7/28/2025 - 8/1/2025

- Complete
 - MEP investigations
 - Duct Cleaning
 - Gas Pipe Demo
 - ALC scope
 - LV Demo
- In Progress - Interior
 - Interior Demolition - 95%
 - Electrical Reroute
 - Steel Fabrication
 - Roof Hydrants
 - Ductwork Installation
- In Progress - Exterior
 - Roofing Replacement - 85%

Key Deliveries

- NG Generator – 12/15/25
- ERUs - 9/26/25



Structural Steel Installation



 LORD AECK SARGENT



Roof Replacement

Balfour Beatty

Progress Photos

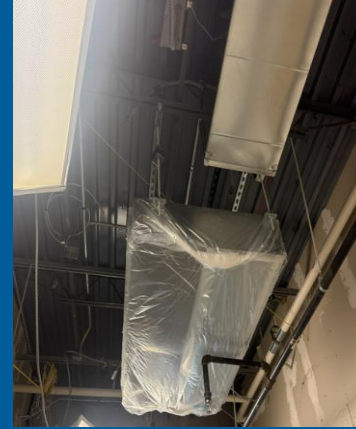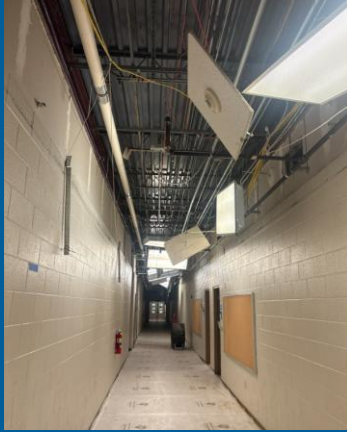

 LORD AECK SARGENT



Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$10,528,700.00
- Progress Billed to Date: \$1,630,405.29 = 15% Completion
- Budget Status: Within GMP

