

# WEST MANOR ELEMENTARY SCHOOL


Weekly Construction Progress Report  
Week 02/01/2021-02/05/2021



**Balfour Beatty**

## Current Activities 02/01/21-02/05/21

- Continue Gymnasium addition roof decking.
- Continue MEPF overhead rough-in at Renovation.
- Continue installation of mechanical and electrical equipment.
- Continue in-wall MEP rough at Renovation.
- Continue gymnasium wall backfill.
- Continue waterproofing as back fill continues.
- Continue interior metal framing at renovation.
- Continue interior and exterior masonry at renovation.
- Start exterior masonry at gymnasium.
- Continue paint and prep at East wing.
- Start paint and prep at North wing.
- Continue roofing replacement.
- Continue hang/tape/finish drywall.
- Continue ceiling grid in SW wing & Cafeteria and MEP trims.
- Prep/place classroom addition footings.
- Start forming classroom addition foundation walls.

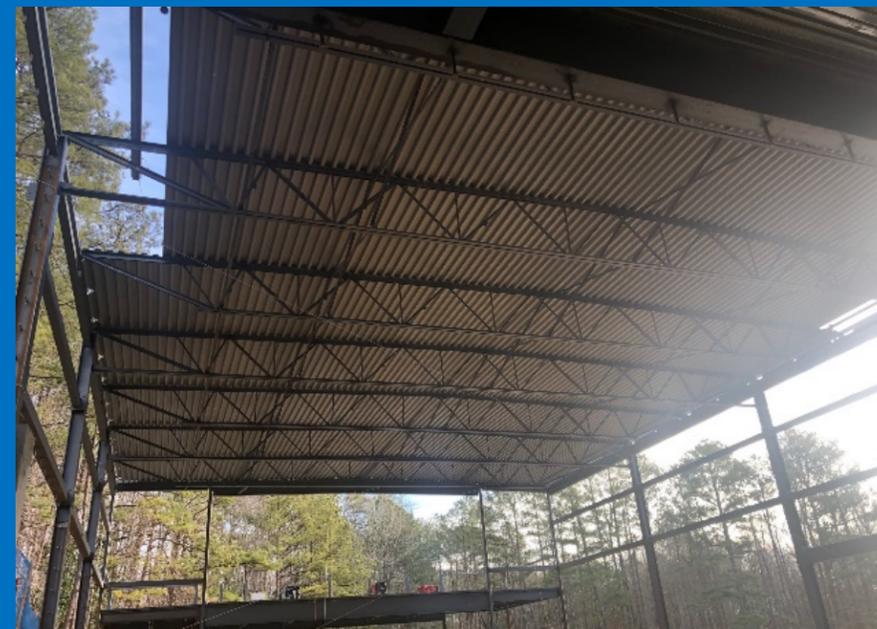

Gymnasium Roof Decking

## Upcoming Activities 02/08/21-02/12/21

- Continue Gymnasium addition roof decking.
- Continue MEPF overhead rough-in at Renovation.
- Continue installation of mechanical and electrical equipment.
- Continue ceiling grid and MEP trims at renovation.
- Continue in-wall MEP rough at Renovation.
- Continue foundation drain and wall backfill (Pending weather)
- Prep/place classroom addition foundation walls (Pending weather)
- Prep/place classroom addition SOG. (Pending weather)
- Continue foundation wall waterproofing. (Pending weather)
- Continue interior metal framing at renovation.
- Continue hang/tape/finish drywall.
- Continue interior and exterior masonry at renovation.
- Continue exterior masonry at gymnasium.
- Continue wall prep and paint.
- Continue roofing replacement.
- Continue admin addition steel.



TPO Roofing Replacement

# Activities



South Gymnasium Wall Backfill



Gymnasium Plumbing Rough In




Gymnasium Exterior CMU Walls



SW Wing Ceiling Grid and MEP Trims



North Wing Steel/CMU Complete and Shoring Removed

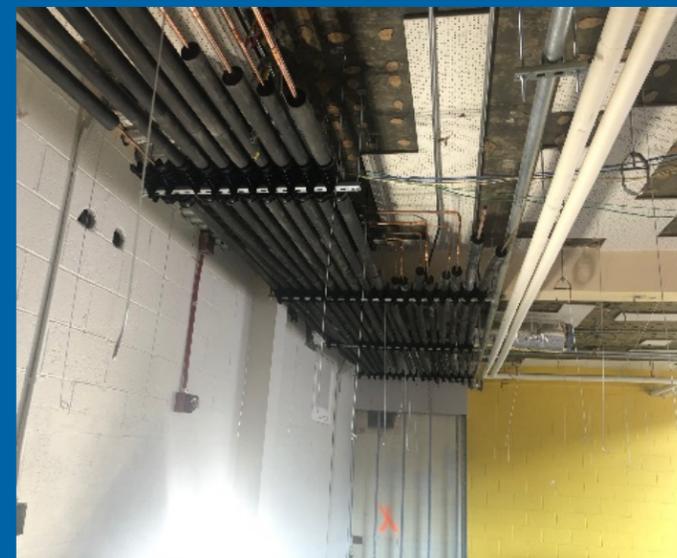

East Wing VRF Installation



## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$11,000,000
- Progress Billed to Date: \$2,711,077
- Budget Status: Within GMP

