

WEST MANOR ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 06/07/2021-06/11/2021



Balfour Beatty

Current Activities 06/07/21-06/11/21

- Continue HVAC equipment start-up and testing.
- Continue installation of electrical panels at gymnasium and terminating wire.
- Continue MEP finish trims (outlets, devices, etc.)
- Continue low voltage installation (fire alarm & security) and testing at gymnasium.
- Continue elevator installation.
- Complete final clean in renovation.
- Complete floor wax in renovation.
- Continue final paint at gymnasium/classroom addition.
- Continue VCT/Carpet installation at gymnasium/classroom addition.
- Complete toilet partition and accessories installation at gymnasium.
- Continue final grade and backfill at gymnasium.
- Complete installation of ground face cap block.
- Continue installation of exterior lighting.
- Continue installation of monument stair railing
- Start installation of casework at gymnasium/classroom addition.
- Start/Complete installation of doors and hardware at gymnasium/classroom addition.
- Start aluminum canopy installation.
- Start underground utilities at entrance.

Upcoming Activities 06/14/21-06/18/21

- Continue HVAC equipment start-up and testing.
- Complete installation of electrical panels at gymnasium and terminating wire.
- Continue MEP finish trims (outlets, devices, etc.)
- Complete low voltage installation (fire alarm & security) and testing at gymnasium.
- Complete elevator installation.
- Complete interior CMU at gymnasium at elevator.
- Continue final paint at gymnasium/classroom addition.
- Complete VCT installation at gymnasium/classroom addition.
- Start installation of remainder of trees.
- Place/Pour Dumpster Pad.
- Place/Pour Media Center Patio
- Place/Pour South Gym Elevation Hardscapes
- Continue underground utilities at entrance.
- Start roofing metal trim at renovation.
- Start exterior paint at existing metal soffits.



Gymnasium South East Elevation Progress



Gymnasium Ramp and Stair Completion




Balfour Beatty

Activities



Gymnasium Stage Lighting Installed

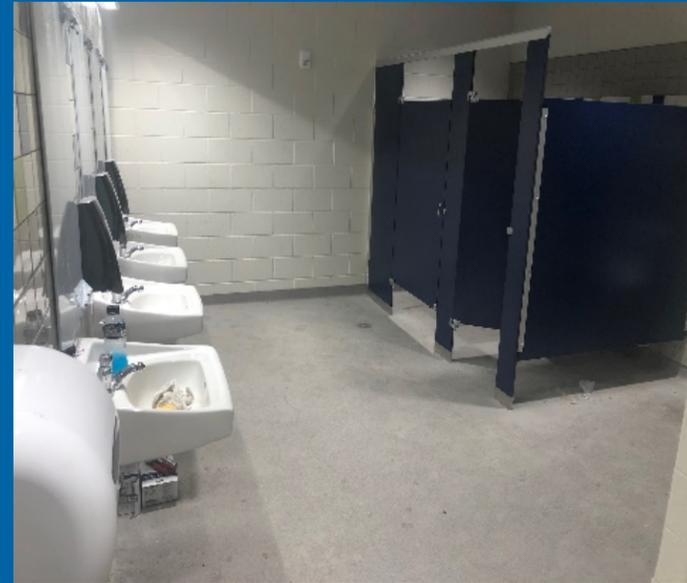

Gymnasium Toilet Partitions and Accessories



Installation of Underground Utilities



Main Entrance Floor Wax Complete



Gymnasium Door & Hardware Installation



Chamfered Block Installation



Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$11,000,000
- Progress Billed to Date: \$8,375,802
- Budget Status: Within GMP

