

# WEST MANOR ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 11/9/20-11/13/20



**Balfour Beatty**

## Current Activities 11/9/20-11/13/20

- Completion of Main Entrance slab on grade addition.
- Completion of Stormtech underground retention system.
- Start rebar/concrete at gymnasium addition footings.
- Interior plumbing underground inspected and prepped for concrete.
- Completion of MEP underground rough at Admin/Entry additions.
- Start MEP overhead rough at SW wing.

## Upcoming Activities 11/16/20-11/20/20

- Continue gymnasium addition footers.
- Start placement of concrete at gymnasium retaining wall.
- Place concrete at admin addition and interior slab on grade pour-backs.
- Continue MEP overhead rough-in at SW Wing
- Continuing selective exterior wall demo.
- Crane mobilization to remove existing HVAC equipment.




Stormtech Underground Drainage System



First Concrete Pour at Gymnasium Footings

# Activities

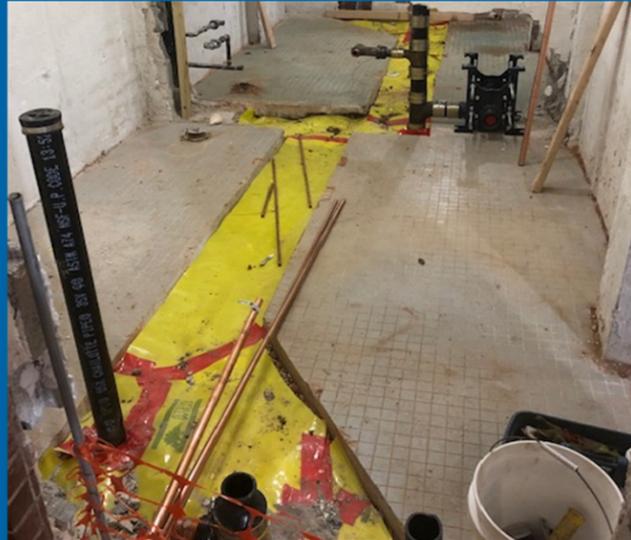

Slab Trenches Prepped for Concrete



Main Entrance Addition Slab on Grade



Underground Storm Structure Backfilled



OH Rough at SW Wing



Continuation of Gymnasium Foundations



Exterior Wall Demo



## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$11,000,000
- Progress Billed to Date: \$979,014.23
- Budget Status: Within GMP

