

# BENTEEN

ELEMENTARY SCHOOL

*Weekly Construction Progress Report  
Week 07/03/2023-07/07/2023*



**Balfour Beatty**

## Current Activities 07/03/2023-07/07/2023


- Connect & Start-up New HVAC Equipment - Ongoing
- Fire Alarm Testing and Troubleshooting – Ongoing
- Final Clean of the Building – Ongoing
- Mechanical Final Inspection
- Plumbing Final Inspection
- Kitchen Health Inspection
- Startup Existing Elevator



Final Clean of the Building

## Upcoming Activities 07/10/23-07/14/23

- Install Temporary Entry / Access Point
- Final Waxing

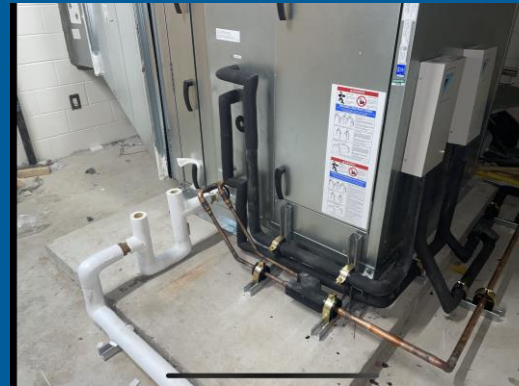

Connect & Start-up New HVAC Equipment

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$7,734,405.60
- Budget Status: Within GMP

